

# Management Report No. 26


## EFDC Building Programme (Phase 4 Sites)



11 November 2021

Updated during meeting - na

Figures updated 11/11/21




AIREMILLER

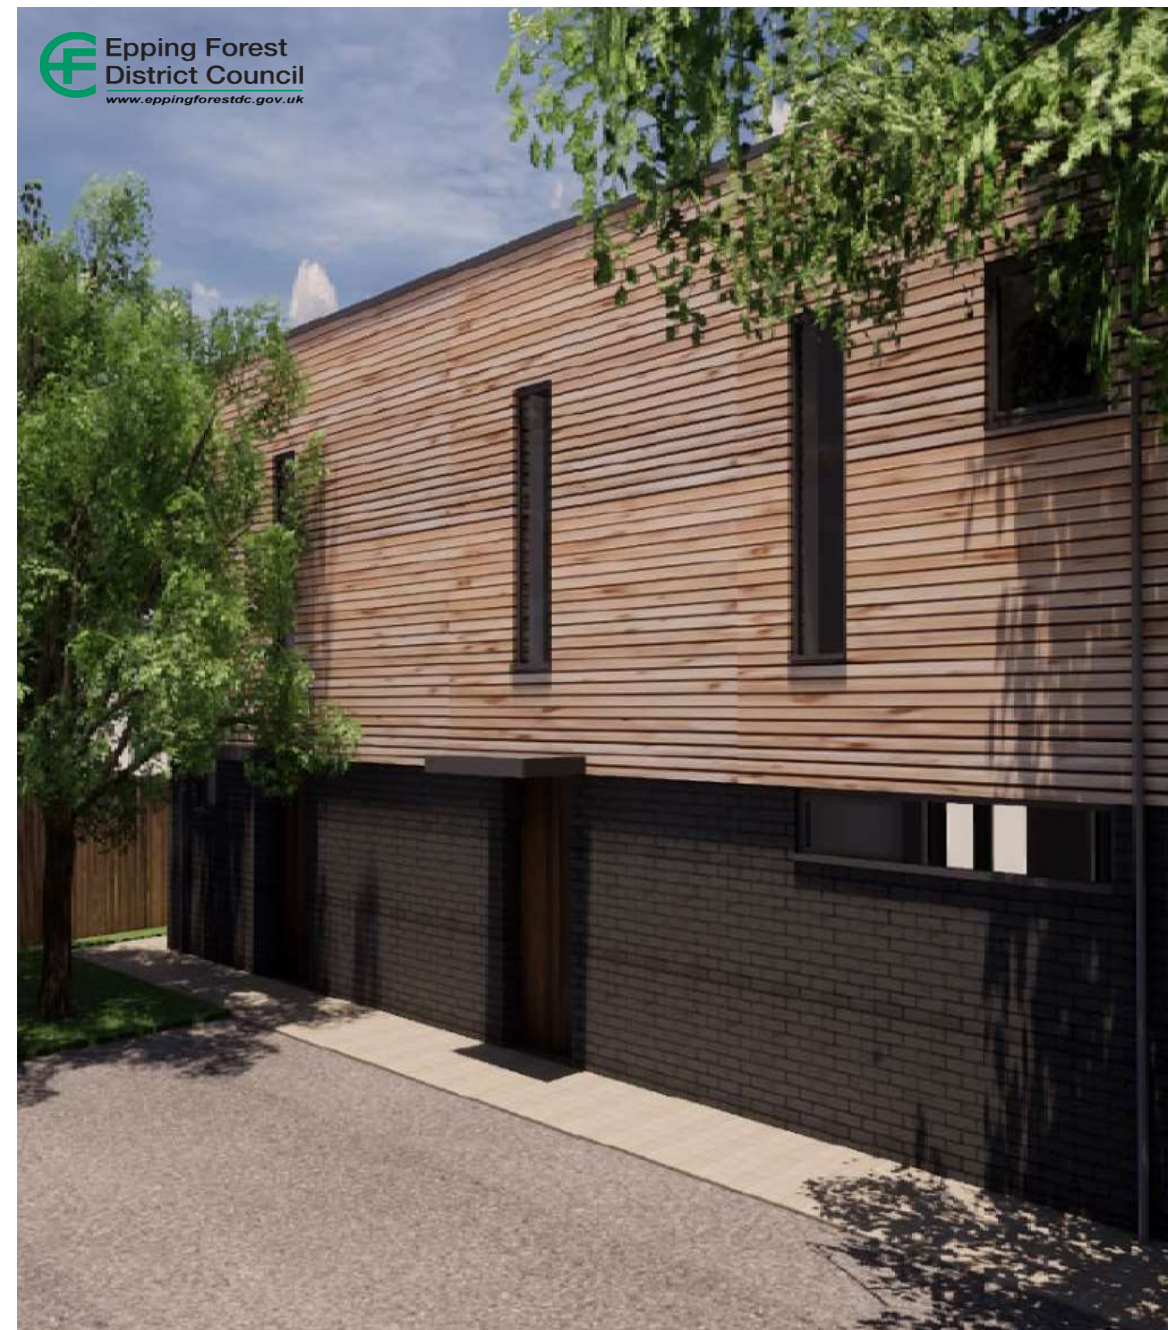

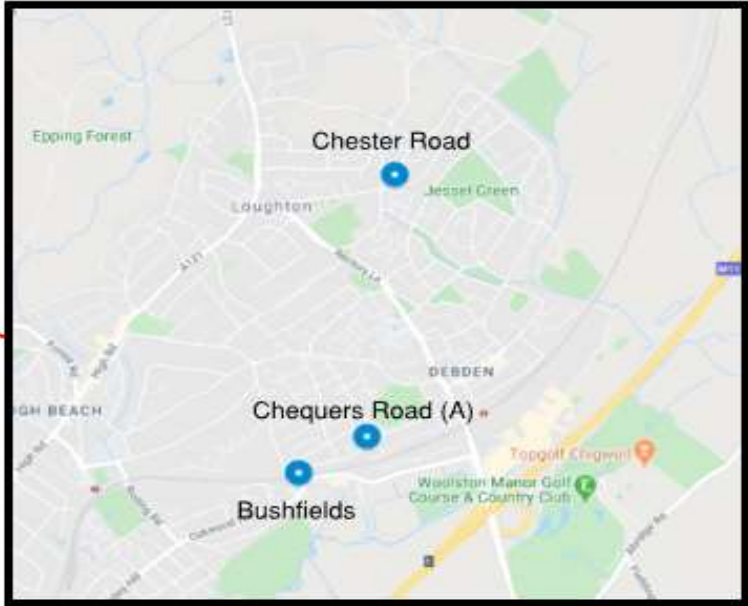
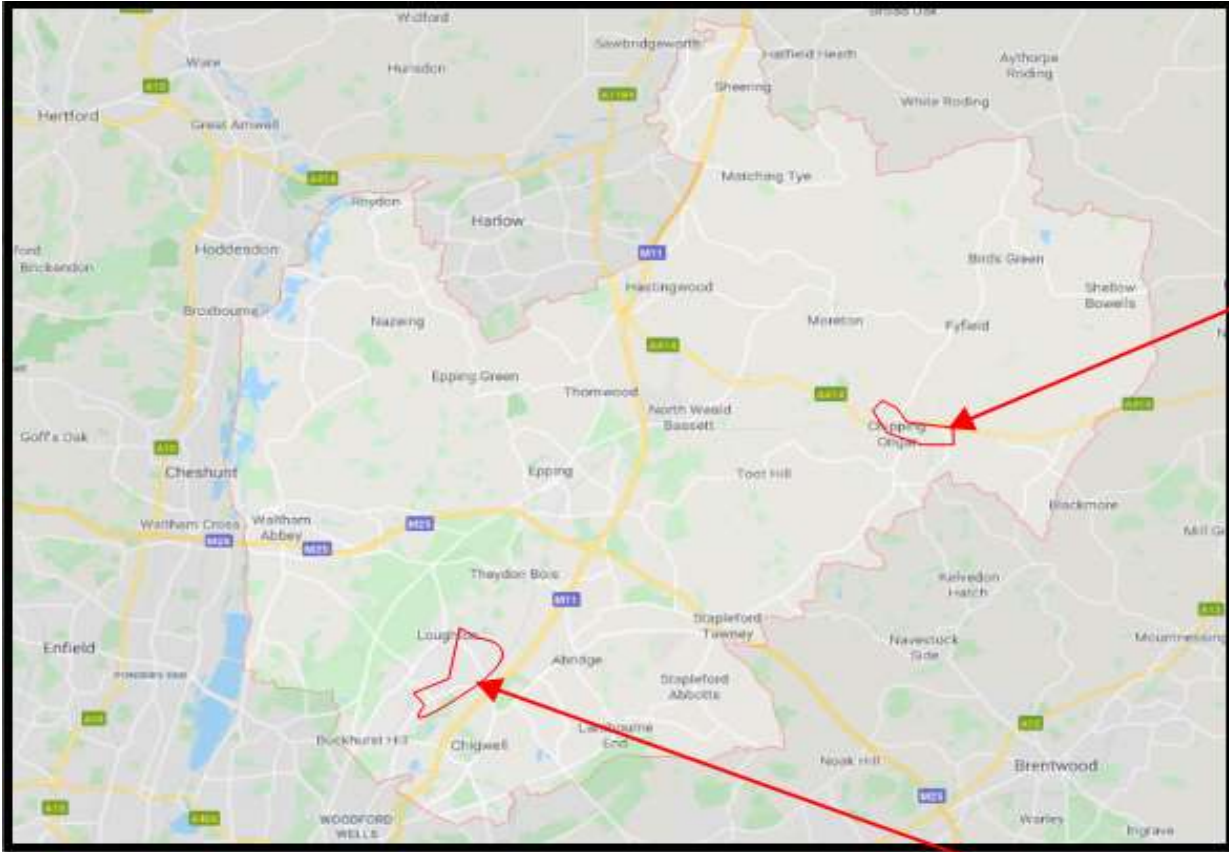


# PHASE 4.1 SITES



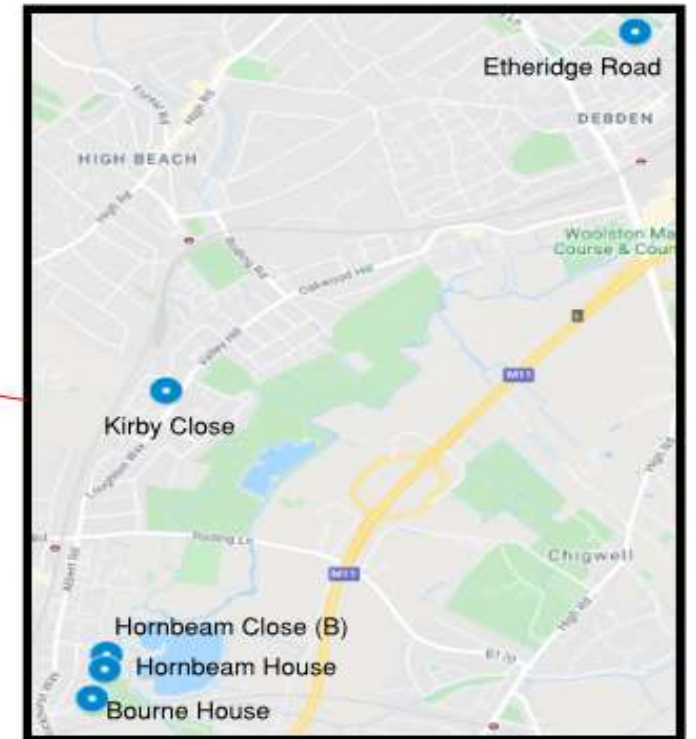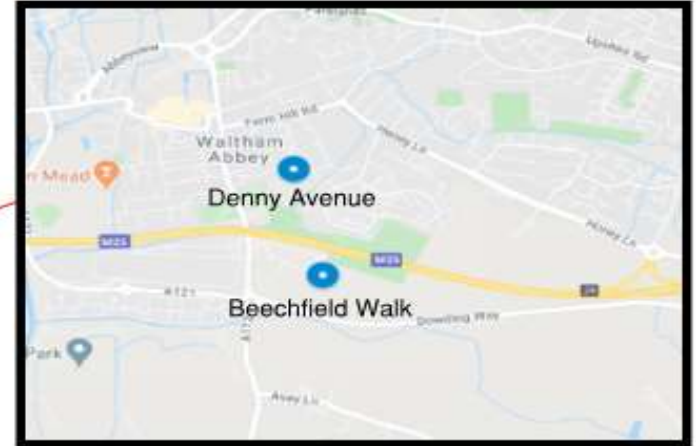
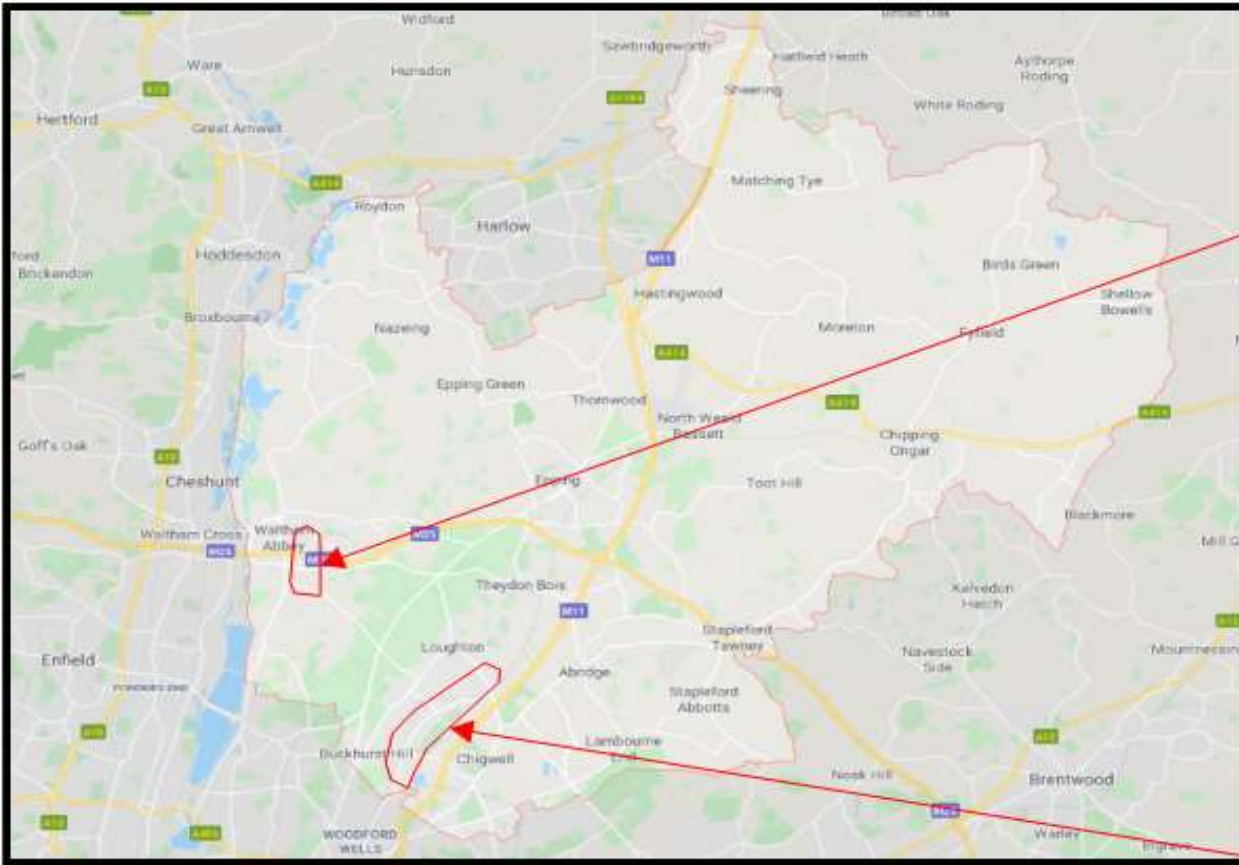


# PHASE 4.2 SITES

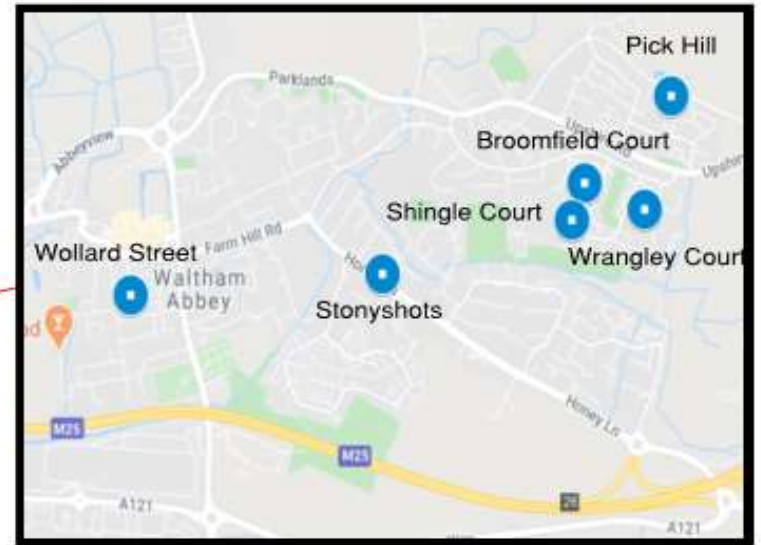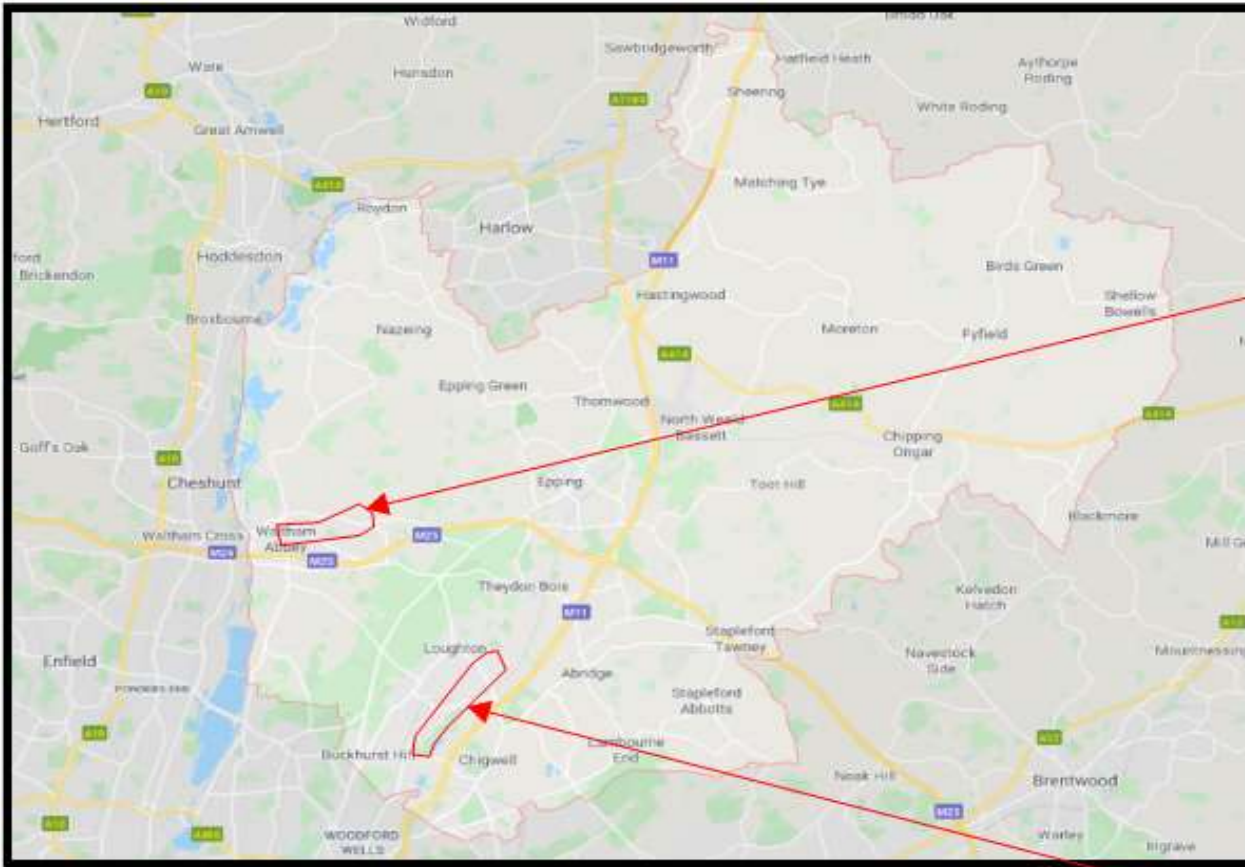

# PHASE 4.3 & 4.4 SITES



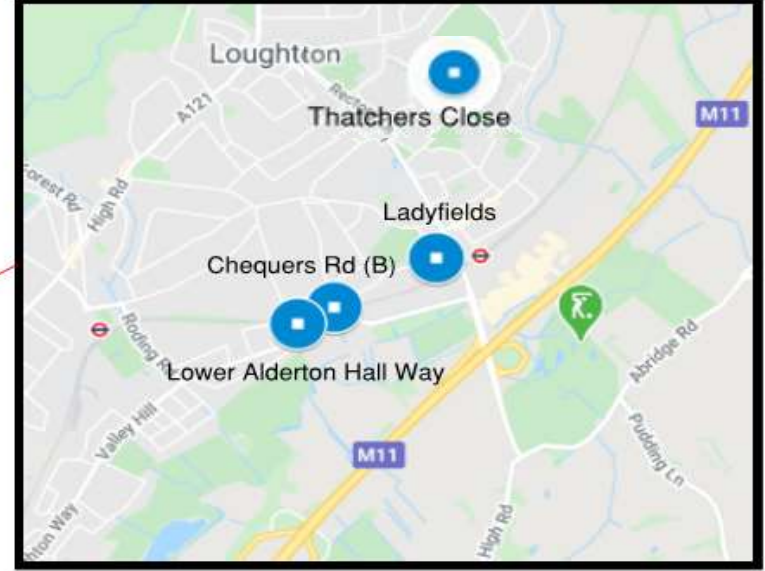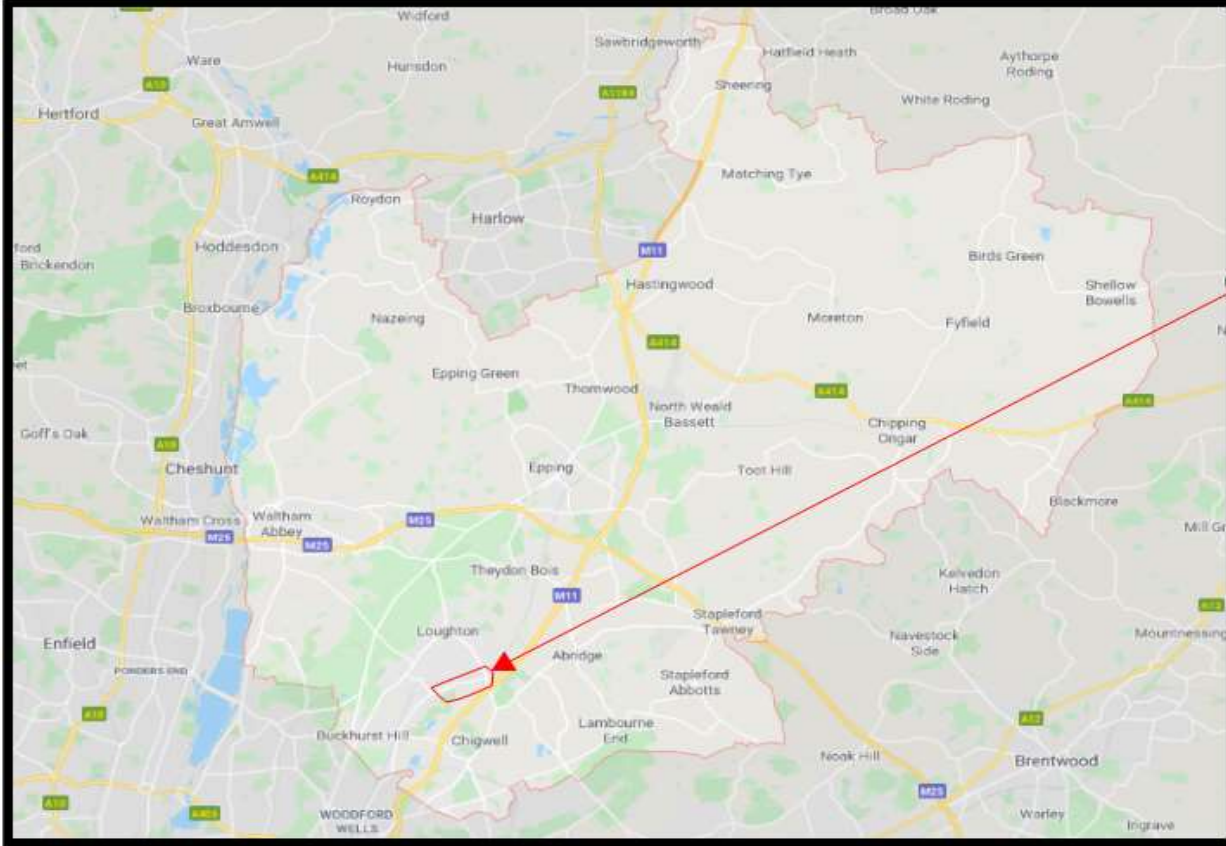

# PHASE 4.4 & 4.5 SITES

## Contents

			Page
<b>Programme Summary</b>			<b>7</b>
Programme Summary - Mix & No. of Homes			8
Current Construction Cost Status			9
CHB Overall Cashflow - 6 Month Overview			10
Key Dates Milestones Summary			11
<b>Package / Site Reviews</b>	<b>Ph</b>	<b>Site Code</b>	<b>12</b>
Chequers Road Site A (Loughton)	4.1	HR124	13
Bushfields (Loughton)	4.1	HR122	16
Chester Road (Loughton)	4.1	HR130	19
Queensway (Ongar)	4.1	HR140	22
Millfield (Ongar)	4.1	HR138	25
Pick Hill (Waltham Abbey)	4.1	HR145	28
Hornbeam Close Site B (Buckhurst Hill)	4.2	HR136	31
Hornbeam House (Buckhurst Hill)	4.2	HR137	34
Bourne House (Buckhurst Hill)	4.2	HR135	37
Etheridge Road (Debden)	4.2	HR127	40
Denny Avenue (Waltham Abbey)	4.2	HR144	43
Beechfield Walk (Waltham Abbey)	4.2	HR142	46
Kirby Close (Loughton)	4.2	HR120	49

	Ph	Site Code	Page
Pentlow Way (Buckhurst Hill)	4.3	HR139	52
Woollard Street (Waltham Abbey)	4.3	HR149	55
Chequers Road Site B (Loughton)	4.4	HR123	58
Ladyfields (Loughton)	4.4	HR125	61
Lower Alderton Hall Lane (Loughton)	4.5	HR121	64

## Programme Summary

## Programme Summary - Mix & No. of Homes

Sites / Codes			Units	RIBA G/W	NIA	GIA	Flats			Houses			Total	Comments - Change Since Last Report
							1b	2b	3b	1b	2b	3b		
Chequers Road Site A (Loughton)	4.1	HR124	3	4	292	302						3	3	
Bushfields (Loughton)	4.1	HR122	2	4	159	162					2		2	
Chester Road (Loughton)	4.1	HR130	3	4	250	263					3		3	
Queensway (Ongar)	4.1	HR140	4	4	200	205				4			4	
Millfield (Ongar)	4.1	HR138	2	4	100	102				2			2	
Pick Hill (Waltham Abbey)	4.1	HR145	2	3	193	201						2	2	
Hornbeam Close Site B (Buckhurst Hill)	4.2	HR136	3	4	118	303						3	3	
Hornbeam House (Buckhurst Hill)	4.2	HR137	2	4	211	163					2		2	
Bourne House (Buckhurst Hill)	4.2	HR135	2	4	142	201						2	2	
Etheridge Road (Debden)	4.2	HR127	3	4	188	261					1	2	3	
Denny Avenue (Waltham Abbey)	4.2	HR144	3	4	198	284					1	2	3	
Beechfield Walk (Waltham Abbey)	4.2	HR142	5	4	284	418					5		5	
Kirby Close (Loughton)	4.2	HR120	4	4	258	373					4		4	
Pentlow Way (Buckhurst Hill)	4.3	HR139	7	4	387	488	6	1					7	
Woollard Street (Waltham Abbey)	4.3	HR149	8	4	438	575	7	1					8	
Chequers Road Site B (Loughton)	4.4	HR123	8	2	520	665	4	4					8	
Ladyfields (Loughton)	4.4	HR125	16	2	990	1,168	12				2	2	16	
Lower Alderton Hall Lane (Loughton)	4.5	HR121	2	4	TBC	TBC				2			2	
<b>Total</b>					<b>4,928</b>	<b>6,134</b>	<b>29</b>	<b>6</b>	<b>0</b>	<b>8</b>	<b>20</b>	<b>16</b>	<b>79</b>	

*RIBA Gateway - This generally refers to the RIBA stage that the project is currently WITHIN.*



## Build / Tender Cost Status (Exc. Fees) - Pre-Contract

Sites / Codes	Units	Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)	Current Total Build Cost (From Site Cost Page)	Comments - Change Since Last Report	
Chequers Road Site A (Loughton)	4.1 HR124	3	tbc	£828,690	£873,967	£45,277	£777,037	£75,567	£852,604	Some variations in process of being agreed.
Bushfields (Loughton)	4.1 HP122	2	tbc	£556,697	£614,054	£57,357	£588,444	£32,941	£621,385	Some variations in process of being agreed.
Chester Road (Loughton)	4.1 HR130	3	tbc	£718,238	£763,319	£45,081	£747,395	£104,213	£851,608	Some variations in process of being agreed.
Queensway (Ongar)	4.1 HR140	4	tbc	£1,120,361	£890,492	-£229,869	£871,309	£39,505	£910,814	Some variations in process of being agreed.
Millfield (Ongar)	4.1 HR138	2	tbc	£351,024	£487,197	£136,173	£501,616	£62,303	£563,919	Some variations in process of being agreed.
Pick Hill (Waltham Abbey)	4.1 HR145	2	tbc	£625,415	£738,613	£113,198	£738,613	£49,011	£787,624	Some variations in process of being agreed.
Hornbeam Close Site B (Buckhurst Hill)	4.2 HR136	3	tbc	£804,225	£972,800	£168,575	£796,102	£0	£796,102	Variations in process of being agreed.
Hornbeam House (Buckhurst Hill)	4.2 HR137	2	tbc	£447,445	£596,885	£149,440	£643,764	£0	£643,764	Variations in process of being agreed.
Bourne House (Buckhurst Hill)	4.2 HR135	2	tbc	£597,832	£646,400	£48,568	£720,149	£0	£720,149	Variations in process of being agreed.
Etheridge Road (Debden)	4.2 HR127	3	tbc	£852,555	£976,925	£124,370	£1,173,281	£0	£1,173,281	Variations in process of being agreed.
Denny Avenue (Waltham Abbey)	4.2 HR144	3	tbc	£771,605	£858,800	£87,195	£860,640	£0	£860,640	Variations in process of being agreed.
Beechfield Walk (Waltham Abbey)	4.2 HR142	5	tbc	£1,087,011	£1,297,200	£210,189	£1,115,482	£0	£1,115,482	Variations in process of being agreed.
Kirby Close (Loughton)	4.2 HR120	4	tbc	£911,559	£1,107,004	£195,445	£1,085,101	£0	£1,085,101	Variations in process of being agreed.
Pentlow Way (Buckhurst Hill)	4.3 HR139	7	tbc	£1,588,896	£1,774,637	£185,741	£1,950,504	£0	£1,950,504	Contract issued
Woollard Street (Waltham Abbey)	4.3 HR149	8	tbc	£1,399,539	£1,556,187	£156,648	£1,662,008	£0	£1,662,008	Contract issued
Chequers Road Site B (Loughton)	4.4 HR123	8	tbc	£1,636,993	£2,623,385	£986,392			£2,623,385	Estimate updated incl Passivhaus, sub station and landscaping
Ladyfields (Loughton)	4.4 HR125	16	tbc	£1,275,879	£3,681,662	£2,405,783			£3,681,662	Estimate updated incl Passivhaus and landscaping
Lower Alderton Hall Lane (Loughton)	4.5 HR121	2	tbc	£507,768	£761,467	£253,699			£761,467	
<b>Total</b>				<b>£16,081,732</b>	<b>£21,220,994</b>	<b>£5,139,262</b>	<b>£14,231,445</b>	<b>£363,540</b>	<b>£21,661,499</b>	

## CHB Overall Cashflow - 6 Month Overview

Date: 11/11/21

Scheme: Epping Phase 4.1 - 4.4

Summary - Overall Cashflow - Excluding Single Unit Sites

Summary - Overall Cashflow	Contract Total	Total Invoiced	Total Remaining	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22	Apr-22
Phase 4.1 - 4.4	£ 25,315,031	£ 9,736,695	£ 15,578,337	£ 895,575	£ 1,031,486	£ 849,377	£ 691,700	£ 662,147	£ 331,352

## Key Dates Milestones Summary

Phase 4.1 completion dates at risk - confirmation required from TSG  
Phase 4.2 completion dates being monitored.  
Phase 4.3 Woollard start pending planning condition discharge  
Phase 4.4 Planning committee dates not known and all dates are pending this.

Sites / Codes	HR	Ph	Units	Planning			RIBA 0-1 Viability Approval		RIBA 2 Completion Date		RIBA 3 Completion Date		RIBA 4 Completion Date		Procurement				Contract		SoS	HO	Comments - Change Since Last Report
				Planned	Actual	Expiry	Planned	Actual	Planned	Actual	Planned	Actual	Planned	Actual	Out	Return	Report	Appro-val	Cooling off Per.	Contract Poss.			
Chequers Road Site A (Loughton)	HR124	4.1	3	-	05/02/16	06/02/19	-	*	-	*	-	19/12/18	17/07/19	08/08/19	09/08/19	27/09/19	11/11/19	16/12/19	30/12/20	05/03/20	31/07/20	08/12/21	Progress slow due to resource availability.
Bushfields (Loughton)	HR122	4.1	2	-	03/05/16	03/05/19	-	*	-	*	-	19/12/18	17/07/19	08/08/19	09/08/19	27/09/19	11/11/19	16/12/19	30/12/20	05/03/20	13/07/20	TBA	Roof leak delayed progress.
Chester Road (Loughton)	HR130	4.1	3	-	04/03/16	04/03/19	-	*	-	*	-	20/12/18	17/07/19	08/08/19	09/08/19	27/09/19	11/11/19	16/12/19	30/12/20	05/03/20	07/09/20	24/01/22	Progress slow due to resource availability.
Queensway (Ongar)	HR140	4.1	4	-	20/06/16	20/06/19	-	*	-	*	-	21/12/18	17/07/19	08/08/19	09/08/19	04/10/19	11/11/19	16/12/19	30/12/20	05/03/20	02/11/20	08/12/21	Progress slow due to resource availability.
Millfield (Ongar)	HR138	4.1	2	-	20/06/16	20/06/19	-	*	-	*	-	21/12/18	17/07/19	08/08/19	09/08/19	04/10/19	11/11/19	16/12/19	30/12/20	05/03/20	30/11/20	31/1/222	Progress slow due to resource availability.
Pick Hill (Waltham Abbey)	HR145	4.1	2	-	25/01/17	25/01/20	-	*	-	*	-	*	17/06/20	23/06/20	24/06/20	14/08/20	11/09/20	23/09/20	07/10/20	04/01/21	15/03/21	14/03/22	Progress slow due to resource availability.
Hornbeam Close Site B (Buckhurst Hill)	HR136	4.2	3	-	04/08/16	04/08/19	-	*	-	*	29/10/19	04/10/19	19/12/19	19/12/19	19/12/19	02/03/20	02/05/20	26/06/20	10/07/20	30/07/20	25/01/21	21/03/22	On site, material availability causing issues.
Hornbeam House (Buckhurst Hill)	HR137	4.2	2	-	04/08/16	04/08/19	-	*	-	*	29/10/19	04/10/19	19/12/19	19/12/19	19/12/19	02/03/20	02/05/20	26/06/20	10/07/20	30/07/20	25/01/21	11/02/22	
Bourne House (Buckhurst Hill)	HR135	4.2	2	-	04/08/16	04/08/19	-	*	-	*	29/10/19	04/10/19	19/12/19	19/12/19	19/12/19	02/03/20	02/05/20	26/06/20	10/07/20	30/07/20	25/01/21	25/02/22	
Etheridge Road (Debden)	HR127	4.2	3	-	30/08/16	30/08/19	-	*	-	*	04/11/19	04/10/19	19/12/19	19/12/19	19/12/19	02/03/20	02/05/20	26/06/20	10/07/20	30/07/20	08/02/21	19/04/22	
Denny Avenue (Waltham Abbey)	HR144	4.2	3	-	25/01/17	25/01/20	-	*	-	*	04/11/19	04/10/19	19/12/19	19/12/19	19/12/19	02/03/20	02/05/20	26/06/20	10/07/20	30/07/20	08/02/21	29/03/22	
Beechfield Walk (Waltham Abbey)	HR142	4.2	5	-	22/03/17	22/03/20	-	*	-	*	04/11/19	04/10/19	19/12/19	19/12/19	19/12/19	02/03/20	02/05/20	26/06/20	10/07/20	30/07/20	08/02/21	08/02/22	
Kirby Close (Loughton)	HR120	4.2	4	-	21/09/16	21/09/19	-	*	-	*	-	*	23/01/20	23/01/20	30/01/20	02/03/20	02/05/20	26/06/20	10/07/20	30/07/20	08/02/21	29/03/22	
Pentlow Way (Buckhurst Hill)	HR139	4.3	7	-	20/12/17	20/12/20	-	*	-	*	-	*	17/06/20	23/06/20	24/06/20	14/08/20	11/09/20	23/09/20	05/05/21	01/06/21	June 22	June 23	Contract signed
Woollard Street (Waltham Abbey)	HR149	4.3	8	-	13/12/17	13/12/20	-	*	-	*	-	*	17/06/20	23/06/20	24/06/20	14/08/20	11/09/20	23/09/20	05/06/21	01/07/21	Feb 22	Feb 23	Contract signed, start pending planning condition approval
Chequers Road Site B (Loughton)	HR123	4.4	8	-	09/02/16	09/02/19	02/05/20	16/05/20	17/07/20	18/08/20	16/10/20	30/10/20	21/01/21		07/01/21	02/04/21	14/05/21	25/06/21	14/07/21	01/08/21	Jan 23	Jan 24	Portfolio approval Nov 2020, planning target 25/12, contract sign July, poss Aug. Planning delay.
Ladyfields (Loughton)	HR125	4.4	16	-	21/09/16	21/09/19	16/12/19	20/02/20	10/07/20		24/07/20	09/09/20	02/01/21		07/01/21	04/03/21	15/04/21	27/05/21	14/07/21	01/08/21	Jan23	Jan 24	Portfolio approval Nov 2020, planning target 14/12, contract sign July, poss Aug. Planning delay
Lower Alderton Hall Lane (Loughton)	HR121	4.5	2	-	04/03/16	04/03/19	-	*	-	*	-	*	19/12/19	19/12/19	03/04/21	29/05/21	10/07/21	21/08/21	04/09/21	09/10/21	Jan 23	Jan 24	Site Tendered - SAC Issue delaying commencement

RIBA Gateway - This generally refers to the RIBA stage that the project is currently WITHIN.

\*= Scheme inherited after original completion of noted RIBA Gateway

## **Package / Site Reviews**



## Chequers Rd A (Loughton) - HR124 - Phase 4.1

(3 x 3B5P Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	1	5	0
Medium Risk	8	0	0

### Actions Complete

### Forthcoming Actions (Month)

- Contract completion date 27/8/21 - Certificate of Non Completion Issued
- Latest planned comp date was 17/9/21 - TSG have stated a revised completion date of 26/11/21 and applied for an EOT to 24/11/21 for which additional detail has been requested.
- Foul drainage alternative connection to 12A agreed with TW, highways approval received - TSG to co-ordinate works with surface water connection
- cash flow for 4.1 sites behind expected, updated version requested for latest completion dates
- NMA now approved
- ground floor wcs to have shower fitted
- Completion date notified as 19/11/21 EOT applied to 12/11/21. Actual date now 8/12/21 but at risk.
- EOT meeting scheduled.

### Change Control Since Last Meeting

- carpets have been added

There will be a general adjustment of Professional Fees on final account which will need to be added onto the Cash Flow figures.

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£828,690.00	£873,967.25	£45,277.25	£777,037.00	£75,567.00

- Control Account (Contingency) Allowance to cover site risks included with Tender Recommendation
- EFDC CHBCC approval of tender recommendation received 19/12/19

### Current RIBA Gateway Position:

Gateway: 4  
Anticipated completion of current gateway: 19/12/2019 (achieved)

### Key Target Dates

Planning/Amendment Submitted: Submitted  
Consent Received: 05/02/2016  
Planning Expiry: 06/02/2019  
Enacted (Y/N): Yes  
Start on Site: 31/07/2020  
Completion: 08/12/2021

## Chequers Rd A (Loughton) - HR124 - Phase 4.1

(3 x 3B5P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£62,717	£62,717	£36,212	£26,507	£0	Remaining includes VFP fees to 2023
2	ECDA, Create, Keegans & OHLA Fees	E160	£59,412	£59,412	£59,412	£0	£0	
3	(Survey Total)	E120	£20,574	£20,574	£20,174	£400	£0	
4	Build Cost	E040	£852,604	£852,604	£745,467	£107,138	£0	
5	(Contingency)	E040	£0	£0	£0	£0	£0	Contingency to be adjusted to maintain "Contract Total" - Flag if at risk. Contingency at risk. Contingency adjusted from meeting with JC. When no contingency contract total will increase. Contingency now expended.
6	CoW	E180	£3,560	£3,560	£3,024	£534	£0	
			<b>£998,867</b>	<b>£998,867</b>	<b>£864,289</b>	<b>£134,579</b>	<b>£0</b>	

## Chequers Rd A (Loughton) - HR124 - Phase 4.1

(3 x 3B5P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	2		EFDC / AML	1	2	2	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed for 29/06/20, although reduced labour to meet social distancing requirements  Further Delay from Contractor Supply Chain - risk increased
Contract Termination COVID-19	10	Covid delays progressa	EFDC / AML	2	5	10	AML	(1) Maintain regular and diligent progress as far as possible ie Design, DTM's, remote site meetings etc. (2)Deed of Variation to the JCT Contract to extend the 2 months suspension period to say 6 or 9 months	Schemes Progressing - Risk Mitigated
<b>Planning Amendments- S96 Non - Material Amendment Agreement</b>									
Planning Amendments- S96 Non Material Amendment Agreement	9	Formal NMA Requested for compliance updates previously agreed	EFDC	3	3	9	ECDA	(1) ECDA to confirm total of height increase and liaise with EFDC planners where necessary (2) Furthermore - proposed realignment of current footprint ot be assessed	Formal NMA now requested. Potential delay subject to submission and approval
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	2	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works	EFDC	1	2	2	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained.  (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced  29/01/20 - Meeting held 20/01/20 PW surveyor / AML / EFDC to discuss RoW and PW matters. EFDC progressing issues and title packs to be issued. 08/06/20 - AML/ OHLA
<b>Reports &amp; Investigations</b>									
Ground Contamination	0	Petrol Interceptors (x3) likely to have associated Hydrocarbon Contamination	Contractor / EFDC	0	0	0	Contractor	(1) Contractor to confirm allowance within tender for removal of interceptors and contaminated soil	Contingency sum confirmed for remediation
Party Walls - awards to adjoining parties	0	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	0	0	0	EFDC / Keegans	(1) Adjoining Owner Award to be signed for 4 Colson Green Only	Confirmation awards confirmed 20/01/20

## Bushfields (Loughton) - HR122 - Phase 4.1

(2 x 2B4P Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	2	5	0
Medium Risk	9	0	0

-

### Actions Complete

#### Forthcoming Actions (Month)

- Variation costs agreed & Instructed
- contract completion date 9/8/21
- proposed completion was 17/9/21 - TSG have stated a revised completion date of 12/11/21 and applied for an EOT to 30/11/21
- roof is leaking through mansafe fixing - Langley have provided a repair system with 25 year warranty retained. This is severely impacting on progress and the completion date is unconfirmed at this stage.
- EOT meeting scheduled

### Change Control Since Last Meeting

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£556,697.00	£614,053.62	£57,356.62	£588,444.00	£32,941.00

- Control Account (Contingency) Allowance to cover site risks included with Tender Recommendation
- EFDC CHBCC approval of tender recommendation received 19/12/19

#### Current RIBA Gateway Position:

Gateway:	4	
Anticipated completion of current gateway:	19/12/2019	(Achieved)

#### Key Target Dates

Planning/Amendment Submitted:	Submitted
Consent Received:	03/05/2016
Planning Expiry	03/05/2019
Enacted (Y/N)	Yes
Start on Site:	13/07/2020
Completion:	TBA



## Bushfields (Loughton) - HR122 - Phase 4.1

(2 x 2B4P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£18,266	£18,266	£17,232	£1,032	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£49,388	£49,388	£49,017	£371	£0	
3	(Survey Total)	E120	£16,268	£16,268	£16,268	£0	£0	
4	Build Cost	E040	£621,385	£621,385	£482,448	£138,936	£0	
5	(Contingency)	E040	£17,689	£17,689	£0	£17,688	£0	
6	CoW	E180	£3,470	£3,470	£3,024	£435	£0	
			<b>£726,466</b>	<b>£726,466</b>	<b>£567,989</b>	<b>£158,462</b>	<b>£0</b>	

## Bushfields (Loughton) - HR122 - Phase 4.1

(2 x 2B4P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	12		EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed for 29/06/20, although reduced labour to meet social distancing requirements  Further Delay from Contractor Supply Chain - risk increased
Contract Termination COVID-19	5	The risk with this Event is that it can give ground for suspension and even termination by both parties after 2 months of suspension.	EFDC / AML	1	5	5	AML	(1) Maintain regular and diligent progress as far as possible ie Design, DTM's, remote site meetings etc. (2) Deed of Variation to the JCT Contract to extend the 2 months suspension period to say 6 or 9 months	Schemes Progressing - Risk Mitigated
<b>Planning Amendments- S96 Non - Material Amendment Agreement</b>									
Planning Amendments- S96 Non Material Amendment Agreement	1	Formal NMA Requested for compliance updates previously agreed	EFDC	1	1	1	ECDA	(1) ECDA to confirm total of height increase and liaise with EFDC planners where necessary (2) Furthermore - proposed realignment of current footprint to be assessed	Formal NMA now requested. Potential delay subject to submission and approval
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	4	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works	EFDC	2	2	4	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained.  (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced  29/01/20 - Meeting held 20/01/20 with PW surveyor / AML / EFDC to discuss RoW and PW matters. EFDC are progressing matters and title plan packs to be issued.  08/06/20 - EFDC have confirmed site cleared of thirds party rights, but 2no. access points could
<b>Statutory Services &amp; Authorities</b>									
Easement Consultation [Incl. TW Build Near/Build Over matters]	0	225mm Foul Sewer running through rear garden. Building designed to accommodate easement.	EFDC	0	0	0	EFDC	EFDC to confirm easement in place and any covenants on the land in terms of access.	Design Mitigated Easement
<b>Reports &amp; Investigations</b>									
Ground Contamination	0	Petrol Interceptors (x1) likely to have associated Hydrocarbon Contamination	Contractor / EFDC	0	0	0	Contractor	(1) Contractor to confirm allowance within tender for removal of interceptors and contaminated soil	Contingency sum confirmed for remediation

## Chester Road (Loughton) - HR130 - Phase 4.1

(3 x 2B4P Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	2	5	0
Medium Risk	6	0	0

### Actions Complete

Non-Material Amendment Application submitted 18th August 2020 - Planners indicated project not started within timescales. However instructed to continue

### Forthcoming Actions (Month)

- Confirm status of planning NMA
- contract completion date agreed at 13/9/21
- completion date 10/9/21 extended to 8/12/21 EOT requested to 2/12/21
- completion date now 24/1/22
- EOT meeting scheduled.

### Change Control Since Last Meeting

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£718,238.00	£763,318.97	£45,080.97	£747,395.00	£104,213.20

- Control Account (Contingency) Allowance to cover site risks included with Tender Recommendation
- EFDC CHBCC approval of tender recommendation received 19/12/19

### Current RIBA Gateway Position:

Gateway: 4  
 Anticipated completion of current gateway: 19/12/2019 (Achieved)

### Key Target Dates

Planning/Amendment Submitted: Submitted  
 Consent Received: 03/05/2016  
 Planning Expiry: 03/05/2019  
 Enacted (Y/N): Yes  
 Start on Site: 07/09/2020  
 Completion: 24/01/2022

## Chester Road (Loughton) - HR130 - Phase 4.1

(3 x 2B4P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£23,004	£23,004	£20,990	£2,014	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£51,972	£51,972	£51,601	£371	£0	
3	(Survey Total)	E120	£21,983	£21,983	£21,983	£0	£0	
4	Build Cost	E040	£851,608	£851,608	£598,961	£252,647	£0	
5	(Contingency)	E040	£0	£0	£0	£0	£0	Contingency adjusted from discussion with JC Contingency now exceeded.
6	CoW	E180	£3,456	£3,456	£2,876	£579	£0	
			<b>£952,024</b>	<b>£952,024</b>	<b>£696,411</b>	<b>£255,611</b>	<b>£0</b>	



## Chester Road (Loughton) - HR130 - Phase 4.1

(3 x 2B4P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	12		EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed for 29/06/20, although reduced labour to meet social distancing requirements  Further Delay from Contractor Supply Chain - risk increased
Contract Termination COVID-19	5	The risk with this Event is that it can give ground for suspension and even termination by both parties after 2 months of suspension.	EFDC / AML	1	5	5	AML	(1) Maintain regular and diligent progress as far as possible ie Design, DTM's, remote site meetings etc. (2) Deed of Variation to the JCT Contract to extend the 2 months suspension period to say 6 or 9 months	Schemes Progressing - Risk Mitigated
<b>Planning Amendments- S96 Non - Material Amendment Agreement</b>									
Planning Amendments- S96 Non Material Amendment Agreement	9	Formal NMA Requested for compliance updates previously agreed	EFDC	3	3	9	ECDA	(1) ECDA to confirm total of height increase and liaise with EFDC planners where necessary (2) Furthermore - proposed realignment of current footprint to be assessed	Formal NMA now requested. Potential delay subject to submission and approval
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	4	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works	EFDC	2	2	4	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained. (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced  29/01/20 - Meeting held 20/01/20 with PW surveyor / AML / EFDC to discuss RoW and PW matters. EFDC are progressing matters and title plan packs to be issued.
<b>Reports &amp; Investigations</b>									
Party Walls - awards to adjoining parties	0	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	0	0	0	EFDC / Keegans	(1) Adjoining Owner Award to be signed for 4 Pyrls Green Only	Confirmation of Notices served and remaining awards confirmed 28.10.19
Flood Risk	6	Flood risk assessment Potential increase of FFL by 300mm	EFDC	3	2	6	Create (Design Team) ECDA	(1) Draft FRA to be issued and reviewed by EFDC drainage (2) ECDA to coordinate any subsequent design change (3) AM to get contractor to price (if required)	Flood Risk established - LLFA have challenged 300mm increase to FFL s. 20/06/20 - Potential agreement for discharge of associated conditions subject to recommendations being incorporated into design.

# Queensway (Ongar) - HR140 - Phase 4.1

(4 x 1 Bed 2p Bungalows)

**Issues / Risks / Early Warning**

Risk Register			
	Risks	Mitigated	Overdue
High Risk	2	3	0
Medium Risk	10	0	0

-

**Actions Complete**

**Forthcoming Actions (Month)**

- contract completion date agreed at 22/11/21
- planned completion date 8/10/21 has been extended to 8/12/21 EOT has been withdrawn.
- completion date confirmed as 8/12/21 but at risk

**Change Control Since Last Meeting**

-

**Financial**

**Construction Cost Summary (E040)**

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£1,120,361.00	£890,492.40	-£229,868.60	£871,309.00	£39,505.00

- Control Account (Contingency) Allowance to cover site risks included with Tender Recommendation
- EFDC CHDCC approval of tender recommendation received 19/12/19

**Current RIBA Gateway Position:**

Gateway: 4  
 Anticipated completion of current gateway: 19/12/2019 (Achieved)

**Key Target Dates**

Planning/Amendment Submitted: Submitted  
 Consent Received: 03/05/2016  
 Planning Expiry: 03/05/2019  
 Enacted (Y/N): Yes  
 Start on Site: 02/11/2020  
 Completion: 08/12/2021

## Queensway (Ongar) - HR140 - Phase 4.1

(4 x 1 Bed 2p Bungalows)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£27,341	£27,341	£25,552	£1,793	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£57,149	£57,149	£56,778	£371	£0	
3	(Survey Total)	E120	£21,642	£21,642	£21,642	£0	£0	
4	Build Cost	E040	£910,814	£910,814	£693,889	£216,925	£0	
5	(Contingency)	E040	£24,480	£24,480	£0	£24,480	£0	
6	CoW	E180	£3,230	£3,230	£2,588	£639	£0	
			<b>£1,044,655</b>	<b>£1,044,655</b>	<b>£800,448</b>	<b>£244,208</b>	<b>£0</b>	

## Queensway (Ongar) - HR140 - Phase 4.1

(4 x 1 Bed 2p Bungalows)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	12		EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed for 29/06/20, although reduced labour to meet social distancing requirements  Further Delay from Contractor Supply Chain - risk increased
Contract Termination COVID-19	5	The risk with this Event is that it can give ground for suspension and even termination by both parties after 2 months of suspension.	EFDC / AML	1	5	5	AML	(1) Maintain regular and diligent progress as far as possible ie Design, DTM's, remote site meetings etc. (2) Deed of Variation to the JCT Contract to extend the 2 months suspension period to say 6 or 9 months	Schemes Progressing - Risk Mitigated
<b>Planning Amendments- S96 Non - Material Amendment Agreement</b>									
Planning Amendments- S96 Non Material Amendment Agreement	3	Formal NMA Requested for compliance updates previously agreed	EFDC	1	3	3	ECDA	(1) ECDA to confirm total of height increase and liaise with EFDC planners where necessary (2) Furthermore - proposed realignment of current footprint to be assessed	Formal NMA now requested. Potential delay subject to submission and approval
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	4	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works	EFDC	1	4	4	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained. (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced  29/01/20 - Meeting held 20/01/20 with PW surveyor / AML / EFDC to discuss RoW and PW matters. EFDC are progressing matters and title plan packs to be issued. 20/06/20 - Potentially 3no. access points to remain,
<b>Statutory Services &amp; Authorities</b>									
Drainage Strategy / Sewer Diversions / Abandonments	12	Final Connections within adjacent EFDC property undetermined	EFDC	3	4	12	EFDC	EFDC to liaise with Residents and advise of leasehold garden areas to be avoided	
<b>Reports &amp; Investigations</b>									
Ground Contamination	0	Remediation Required for elevated levels of ACMs noted in soil	Contractor / EFDC	0	0	0	Contractor	(1) Contractor to confirm allowance within tender for removal of contaminated soil	Contingency sum confirmed for remediation

## Millfield (High Ongar) - HR138 - Phase 4.1

(2 x 1 bed 2p Bungalows)

### Issues / Risks / Early Warning

Risk Register	Risks	Mitigated	Overdue
High Risk	2	3	0
Medium Risk	11	0	0

### Actions Complete

-

### Forthcoming Actions (Month)

- Actual start on site 21/12/20 (not 30/11/20 as agreed)
- Contract completion date 22/11/21
- planned completion has been extended to 31/1/22 EOT has been withdrawn
- completion date is at risk
- nr 50 has queried the boundary line

### Change Control Since Last Meeting

-

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£351,024.00	£487,197.05	£136,173.05	£501,616.00	£62,303.00

- Control Account (Contingency) Allowance to cover site risks included with Tender Recommendation
- EFDC CHBCC approval of tender recommendation received 19/12/19

### Current RIBA Gateway Position:

Gateway: 4  
Anticipated completion of current gateway: 19/12/2019 (Achieved)

### Key Target Dates

Planning/Amendment Submitted: Submitted  
Consent Received: 03/05/2016  
Planning Expiry: 03/05/2019  
Enacted (Y/N): Yes  
Start on Site: 30/11/2020  
Completion: 31/1/222

## Millfield (High Ongar) - HR138 - Phase 4.1

(2 x 1 bed 2p Bungalows)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£23,582	£23,582	£21,451	£2,130	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£37,143	£37,143	£37,143	£0	£0	
3	(Survey Total)	E120	£24,134	£24,134	£24,134	£0	£0	
4	Build Cost	E040	£563,919	£563,919	£369,621	£194,298	£0	
5	(Contingency)	E040	£0	£0	£0	£0	£0	All contingency used
6	CoW	E180	£3,050	£3,050	£1,708	£1,344	£0	
			<b>£651,828</b>	<b>£651,828</b>	<b>£454,057</b>	<b>£197,772</b>	<b>£0</b>	



## Millfield (High Ongar) - HR138 - Phase 4.1

(2 x 1 bed 2p Bungalows)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	12		EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed for 29/06/20, although reduced labour to meet social distancing requirements  Further Delay from Contractor Supply Chain - risk increased
Contract Termination COVID-19	5	The risk with this Event is that it can give ground for suspension and even termination by both parties after 2 months of suspension.	EFDC / AML	1	5	5	AML	(1) Maintain regular and diligent progress as far as possible ie Design, DTM's, remote site meetings etc. (2)Deed of Variation to the JCT Contract to extend the 2 months suspension period to say 6 or 9 months	Schemes Progressing - Risk Mitigated
<b>Planning Amendments- S96 Non - Material Amendment Agreement</b>									
Planning Amendments- S96 Non Material Amendment Agreement	6	Formal NMA Requested for compliance updates previously agreed	EFDC	2	3	6	ECDA	(1) ECDA to confirm total of height increase and liaise with EFDC planners where necessary (2) Furthermore - proposed realignment of current footprint ot be assessed	Formal NMA now requested. Potential delay subject to submission and approval
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	8	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works	EFDC	2	4	8	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained. (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced  29/01/20 - Meeting held 20/01/20 with PW surveyor / AML / EFDC to discuss RoW and PW matters. EFDC are progressing matters and title plan packs to be issued.
<b>Reports &amp; Investigations</b>									
Ground Contamination	2	Petrol Interceptors (x1) likely to have associated Hydrocarbon Contamination . Potential asbestos under garage slab	Contractor / EFDC	1	2	2	Contractor	(1) Contractor to confirm allowance within tender for removal of interceptors and contaminated soil	Contingency sum confirmed for remediation

## Pick Hill (Waltham Abbey) - HR145 - Phase 4.3

(2 x 3B5P Houses)

Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	1	0	0
Medium Risk	38	0	0

**Actions Complete**

- Pre start meeting held 21/1/21
- TSG took site possession 18/1/21
- price of drainage alterations agreed and instruction issued
- TW diversion approved

**Forthcoming Actions (Month)**

- start and completion dates agreed 15 March 2021 to 14 March 2022
- landscape pre start condition to discharge by TSG
- programme received
- review boundary retaining to main road
- drainage off site has been cctv`ed and routes are clear but will be jetted to remove minor debris
- postal address to confirm
- piling delayed initial progress

**Change Control Since Last Meeting**

Financial

**Construction Cost Summary (E040)**

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£625,415.00	£738,612.63	£113,197.63	£738,613.00	£49,011.00

- Order of cost completed and issued Aug 20 construction cost revised
- ` Tender report issue date 18/9/20

Current RIBA Gateway Position:

Gateway: 4  
 Anticipated completion of current gateway: 30/10/20

Key Target Dates

Planning/Amendment Submitted: Submitted  
 Consent Received: 25/01/2017  
 Planning Expiry: 25/01/2020  
 Enacted (Y/N): Yes  
 Start on Site: 15/03/2021 tbc  
 Completion: 14/03/2022

## Pick Hill (Waltham Abbey) - HR145 - Phase 4.3

(2 x 3B5P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£17,826	£17,826	£13,666	£4,166	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£40,770	£40,770	£39,865	£905	£0	
3	(Survey Total)	E120	£22,492	£22,492	£22,492	£0	£0	
4	Build Cost	E040	£787,624	£787,624	£307,241	£480,381	£0	
5	(Contingency)	E040	£10,989	£10,989	£0	£10,990	£0	
6	CoW	E180	£11,800	£11,800	£990	£10,805	£0	
			<b>£891,501</b>	<b>£891,501</b>	<b>£384,254</b>	<b>£507,247</b>	<b>£0</b>	

## Pick Hill (Waltham Abbey) - HR145 - Phase 4.3 (2 x 3B5P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Planning Approvals</b>									
Consultation Issues - Planning Expiration	0	Planning Permission due to expire 25/01/20	EFDC	0	0	0	ECDA / EFDC	(1) ECDA to confirm issue / validation of Phase 1 contamination Report (2) EFDC to confirm soft demolition works commenced	Planning Enacted
<b>Planning Amendments- S96 Non - Material Amendment Agreement</b>									
Planning Amendments- S96 Non Material Amendment Agreement	0	Formal NMA Requested for compliance updates previously agreed	EFDC	0	3	0	ECDA	(1) ECDA to confirm total of height increase and liaise with EFDC planners where necessary (2) Furthermore - proposed realignment of current footprint ot be assessed	NMA application made
<b>Statutory Services &amp; Authorities</b>									
Drainage Strategy / Sewer Diversions / Abandonments	0	Drainage Strategy to be determined. Pick Hill - Potential Watercourse opposite site entrance identified. Connection to existing Foul / Storm runs difficult due to distance from	EFDC	0	4	0	Create (Civil)	(1) Drainage strategy and points of connection to existing sewers to be established, abandonments / diversions to be identified	Further Survey to Surface Water Run proposed for Diversion
FW & SW sewer capacity checked	4	No capacity in existing foul or storm Pick Hill - due to rural location of development site, capacity a risk	EFDC	2	2	4	Create (Civil)	(1) Drainage strategy and points of connection to existing sewers to be established, abandonments / diversions to be identified	
<b>Reports &amp; Investigations</b>									
Ground Contamination	3	All sites identified as to having ACMs in made ground.	Contractor / EFDC	1	3	3	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards. (2) Ground Gas monitoring to be carried out on potentially effected sites subject to lab testing of impacted sites (3) Remediation Method Statements to be issued where required	
Trees	4	Trees within vicinity or boundary of site that could impact construction proposals.	EFDC	1	4	4	ECDA	(1) Instruction of Arboricultural Surveys to provide comprehensive survey to all sites. Tree Protection Plans & method Statements also commissioned (2) Survey Results to be coordinated with design team to mitigate impact of root protection zones (3) Pick Hill - Liaison with owner of TPO tree's to entrance	
Traffic Management / Site Access	4	Pick Hill is single lane carriageway - site logisitcs and access constrained	EFDC	1	4	4	AML	(1) AML to procure Traffic Management and Logistics Survey (2) Survey Results to be assessed and any issues notd incorporated into Employers Requirements	
Party Walls - awards to adjoining parties	3	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	1	3	3	EFDC / Keegans	(1) Notices to be served to adjacent properties (2) PW Surveyor to advise on objections / concerns	
<b>Construction &amp; Procurement</b>									
Programmes - Delays due COVID-19	16	Pre-construction Design Programme Delay to Due Diligence, potential start on site	EFDC / AML	4	4	16	AML	(1) AML preparing programme options, for Stage 4.1 Design schemes and planning redesign schemes. (2) AML to monitor and track government advice on COVID-19	

## Hornbeam Close B (Buckhurst Hill) - HR136 - Phase 4.2

(3 x 3B5P Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	1	2	0
Medium Risk	34	1	0

### Actions Complete

### Forthcoming Actions (Month)

- All 4.2 sites - Start dates contract 1 - 25/1/21 to 4/2/22
- Dates contract 2 11/1/21 to 10/1/22
- Dates delayed due to planning condition discharge by approx 2 weeks
- revised programme received Stated completion date 21/3/22 due to drainage and retaining walls
- retaining wall details have been reviewed and alternative RC proposals agreed, costs breakdown awaited
- variations costs have been received with the valuations, the break down has been received and these currently appear within the contingency figure.
- most have been agreed and instructions to be issued

### Change Control Since Last Meeting

-

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£804,225.00	£972,800.00	£168,575.00	£796,102.00	

- AML issued Tender Report 04/05/20 - Tender Costs noted
- Risk Items identified have had additional costs allocated in Client Contingency Control budget

### Current RIBA Gateway Position:

Gateway:	4	
Anticipated completion of current gateway:	02/07/20	(Achieved)

### Key Target Dates

Planning/Amendment Submitted:	Submitted
Consent Received:	04/08/2016
Planning Expiry	04/08/2019
Enacted (Y/N)	Yes
Start on Site:	25/01/2021
Completion:	21/03/2022

## Hornbeam Close B (Buckhurst Hill) - HR136 - Phase 4.2

(3 x 3B5P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£19,091	£19,092	£16,157	£2,935	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£50,785	£50,785	£49,492	£1,293	£0	
3	(Survey Total)	E120	£22,538	£22,538	£22,538	£0	£0	
4	Build Cost	E040	£796,102	£796,102	£618,961	£177,140	£0	
5	(Contingency)	E040	£65,000	£65,000	£0	£65,000	£0	
6	CoW	E180	£4,690	£4,690	£1,530	£3,152	£0	
			<b>£958,207</b>	<b>£958,207</b>	<b>£708,678</b>	<b>£249,520</b>	<b>£0</b>	



## Hornbeam Close B (Buckhurst Hill) - HR136 - Phase 4.2

(3 x 3B5P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19- Delays	12	Based on current government advice we are expecting a 3-month delay currently although social distancing may be in effect for up to 6 months	EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed targeted for July, although reduced labour to meet social distancing requirements
<b>Planning Amendments- S73 Minor Material Amendment Agreement</b>									
Planning Amendments- S73 Minor Material Amendment Agreement	0	To ensure technically the houses meet the statutory floor to ceiling heights together with raising the building due to flood risk - risk of having to submit a S.73 application to address changes	EFDC	0	0	0	ECDA	(1) ECDA to confirm total of height increase and liaise with EFDC planners where necessary (2) Furthermore - proposed realignment of current footprint to be assessed	NMA application issued
<b>Statutory Services &amp; Authorities</b>									
Easement Consultation [Incl.TW Build Near/Build Over matters]	0	Build-over or easement consultation required Thames Water Pumping Station - liaison for any easement and assume 24hr access requirements.	EFDC	0	0	0	Create (Civil)	(1) EFDC to confirm easement in place and any covenants on the land in terms of access. (2) Create to liaise with Thames Water to ascertain access requirements	Update @ 01/11/19 - Create have confirmed: TW have <b>no rights</b> over the access roads re pumping station (they requested, wherever possible, for the developer to consider sufficient tanker access to the station as part of the design of the site).
Drainage Strategy / Sewer Diversions / Abandonments	0	Adopted Foul Pipe identified routing through current building footprint	EFDC	0	0	0	Create (Civil)	(1) Create to review asset plans and liaise with Thames Water for direction. (2) Create to apply for S.185 Diversion (3) Create to coordinate civil / structural design accommodate diversion.	Update @ 01/11/19 - Create have confirmed: Diversion option to be TW preference for the foul - S.185 application to be progressed - circa 6-9 months period noted
<b>Reports &amp; Investigations</b>									
Ground Contamination	4	All sites identified as to having ACMs in made ground. Hornbeam Close (Site B) is within 250m of Landfill Sites - Ground gases likely to be present.	Contractor / EFDC	2	2	4	Contractor		No Ground Gas identified - risk reduced however contamination likely
Party Walls - awards to adjoining parties	0	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	0	0	0	EFDC / Keegans	(1) Notices to be served to adjacent properties (2) PW Surveyor to advise on objections / concerns	Notices Served

## Hornbeam House (Buckhurst Hill) - HR137 - Phase 4.2

(2 x 2B4P Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	0	3	0
Medium Risk	38	2	0

### Actions Complete

-

### Forthcoming Actions (Month)

-

- pre start conditions approved 13/1/21
- Dates delayed due to planning condition discharge by approx 2 weeks
- revised programme received 9/2/21 Stated completion date 11/2/22 due to drainage and retaining
- variations costs have been received with the valuations, the break down has been received and these currently appear within the contingency figure.

### Change Control Since Last Meeting

-

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£447,445.00	£596,885.00	£149,440.00	£643,764.23	-£0.23

- AML issued Tender Report 04/05/20 - Tender Costs noted
- Risk Items identified have had additional costs allocated in Client Contingency Control budget

### Current RIBA Gateway Position:

Gateway:	4	
Anticipated completion of current gateway:	02/07/20	(Achieved)

### Key Target Dates

Planning/Amendment Submitted:	Submitted
Consent Received:	04/08/2016
Planning Expiry	04/08/2019
Enacted (Y/N)	Yes
Start on Site:	25/01/2021
Completion:	11/02/2022

## Hornbeam House (Buckhurst Hill) - HR137 - Phase 4.2

(2 x 2B4P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£15,741	£15,741	£13,368	£2,373	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£40,371	£40,371	£39,325	£1,046	£0	
3	(Survey Total)	E120	£17,723	£17,723	£17,723	£0	£0	
4	Build Cost	E040	£643,764	£643,764	£521,606	£122,160	£0	
5	(Contingency)	E040	£60,000	£60,000	£0	£60,000	£0	
6	CoW	E180	£4,592	£4,592	£1,530	£3,056	£0	
			<b>£782,191</b>	<b>£782,191</b>	<b>£593,552</b>	<b>£188,635</b>	<b>£0</b>	

## Hornbeam House, Buckhurst Hill - HR137 - Phase 4.2

(2 x 2B4P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	12	Based on current government advice we are expecting a 3-month delay currently although social distancing may be in effect for up to 6 months	EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed targeted for July, although reduced labour to meet social distancing requirements
<b>Reports &amp; Investigations</b>									
Ground Contamination	4	All sites identified as to having ACMs in made ground. Hornbeam House is within 250m of Landfill Sites - Ground gases likely to be present.	Contractor / EFDC	2	2	4	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards. (2) Ground Gas monitoring to be carried out on potentially effected sites subject	No Ground Gas identified - risk reduced however contamination likely
Unexploded Ordnance	4	Epping is high risk borough for Unexploded Ordnance <i>Identified as Medium Risk Site</i>	Contractor / EFDC	1	4	4	Contractor / UXO	(1) Ensure appointment of UXO specialist watching brief for shallow excavations to all sites (2) Intrusive magnetometer survey for any piling / borehole works to	29/01/20: To be monitored on tender returns - allowance made for attendance of UXO specialist
Party Walls - awards to adjoining parties	0	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	0	0	0	EFDC / Keegans	(1) Notices to be served to adjacent properties (2) PW Surveyor to advise on objections / concerns	No Party Wall Awards on site

## Bourne House (Buckhurst Hill) - HR135 - Phase 4.2

(2 x 3B5P Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	1	5	0
Medium Risk	33	3	0

### Actions Complete

### Forthcoming Actions (Month)

- Dates delayed due to planning condition discharge by approx 2 weeks
- revised programme received Stated completion date 25/2/22
- Retaining walls agreed to be RC
- Pumping station not to be adopted, alternative routes via rugby club have been investigated and not viable alternatives - specification of upgraded pumps has been agreed
- labour & material supply is causing delays
- variations costs have been received with the valuations, the break down has been received and these currently appear within the contingency figure.

### Change Control Since Last Meeting

-

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£597,832.00	£646,400.00	£48,568.00	£720,149.16	-£0

- AML issued Tender Report 04/05/20 - Tender Costs noted
- Risk Items identified have had additional costs allocated in Client Contingency Control budget

### Current RIBA Gateway Position:

Gateway:	4	
Anticipated completion of current gateway:	02/07/20	(Achieved)

### Key Target Dates

Planning/Amendment Submitted:	Submitted
Consent Received:	04/08/2016
Planning Expiry	04/08/2019
Enacted (Y/N)	Yes
Start on Site:	25/01/2021
Completion:	25/02/2022

## Bourne House (Buckhurst Hill) - HR135 - Phase 4.2

(2 x 3B5P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£18,615	£18,615	£15,960	£2,655	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£42,629	£42,629	£41,459	£1,170	£0	
3	(Survey Total)	E120	£19,515	£19,515	£19,515	£0	£0	
4	Build Cost	E040	£720,149	£720,149	£513,199	£206,950	£0	
5	(Contingency)	E040	£65,000	£65,000	£0	£65,000	£0	
6	CoW	E180	£4,592	£4,592	£1,530	£3,056	£0	
			<b>£870,500</b>	<b>£870,500</b>	<b>£591,663</b>	<b>£278,831</b>	<b>£0</b>	



## Bourne House (Buckhurst Hill) - HR135 - Phase 4.2

(2 x 3B5P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	12	Based on current government advice we are expecting a 3-month delay currently although social distancing may be in effect for up to 6 months	EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed targeted for July, although reduced labour to meet social distancing requirements
<b>Planning Approvals</b>									
Planning Amendments- S73 Minor Material Amendment Agreement	0	Current approved plans proposed shift of building back circa 1m to present improved frontage	EFDC	0	0	0	ECDA/ Create	ECDA to confirm realignment and liaise with EFDC planners where necessary	Update @ 01/11/19 - Agreed minor realignment and covered with design development - risk reduced
<b>Reports &amp; Investigations</b>									
Ground Contamination	4	All sites identified as to having ACMS in made ground. Hornbeam House is within 250m of Landfill Sites - Ground gases likely to be present.	Contractor / EFDC	2	2	4	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards.  (2) Ground Gas monitoring to be carried out on potentially effected	No Ground Gas identified - risk reduced however contamination likely
Party Walls - awards to adjoining parties	0	Party Wall Adjacent Excavation and Line of Junction Awards required  Sports Pavilion to Eastern Boundary - PW award for adjacent excavation / foundation required	EFDC	0	4	0	EFDC / Keegans	(1) Notices to be served to adjacent properties  (2) PW Surveyor to advise on objections / concerns	Notices Served

## Etheridge Road (Debden) - HR127 - Phase 4.2

(1 x 2B3P Bungalow & 2 x 3B5P Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	2	3	0
Medium Risk	32	3	0

### Actions Complete

### Forthcoming Actions (Month)

- pre start conditions approved 13/1/21
- completion date 19/4/22
- boundary walls have been assessed and new RC retaining cast or the existing adapted as appropriate
- monitor completion date for Homes England funding
- Sprinkler required for houses - a larger main may be a better option than tanks - Indecon to confirm costs
- variations costs have been received with the valuations, the break down has been received and these currently appear within the contingency figure. These have been agreed and will be instructed.

### Change Control Since Last Meeting

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£852,555.00	£976,925.00	£124,370.00	£1,173,281.00	

- AML issued Tender Report 04/05/20 - Tender Costs noted
- Risk Items identified have had additional costs allocated in Client Contingency Control budget

### Current RIBA Gateway Position:

Gateway:	4	
Anticipated completion of current gateway:	02/07/20	(Achieved)

### Key Target Dates

Planning/Amendment Submitted:	Submitted
Consent Received:	30/08/2016
Planning Expiry	30/08/2019
Enacted (Y/N)	Yes
Start on Site:	11/01/2021
Completion:	19/04/2022

## Etheridge Road (Debden) - HR127 - Phase 4.2

(1 x 2B3P Bungalow & 2 x 3B5P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£24,925	£24,925	£21,323	£3,602	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£53,536	£53,536	£52,510	£1,026	£0	
3	(Survey Total)	E120	£41,429	£41,429	£41,429	£0	£0	
4	Build Cost	E040	£1,173,281	£1,173,281	£918,745	£254,538	£0	
5	(Contingency)	E040	£100,000	£100,000	£0	£100,002	£0	
6	CoW	E180	£4,690	£4,690	£1,530	£3,159	£0	
			<b>£1,397,861</b>	<b>£1,397,861</b>	<b>£1,035,537</b>	<b>£362,327</b>	<b>£0</b>	

## Etheridge Road (Debden) - HR127 - Phase 4.2

(1 x 2B3P Bungalow & 2 x 3B5P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	12	Based on current government advice we are expecting a 3-month delay currently although social distancing may be in effect for up to 6 months	EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed targeted for July, although reduced labour to meet social distancing requirements
<b>Reports &amp; Investigations</b>									
Ground Contamination	4	All sites identified as to having ACMs in made ground. Hornbeam Close (Site B) is within 250m of Landfill Sites - Ground gases likely to be present.	Contractor / EFDC	2	2	4	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards.  (2) Ground Gas monitoring to be carried out on potentially effected sites	No Ground Gas identified - risk reduced however contamination likely
Party Walls - awards to adjoining parties	3	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	1	3	3	EFDC / Keegans	(1) Notices to be served to adjacent properties  (2) PW Surveyor to advise on objections / concerns	Update Received - Conditon Surveys Completed - Awards in place

## Denny Avenue (Waltham Abbey) - HR144 - Phase 4.2

(1 x 2B4p House & 2 x 3B5p Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	1	2	0
Medium Risk	36	4	0

### Actions Complete

### Forthcoming Actions (Month)

- pre start conditions approved 13/1/21
- Completion date 29/3/22
- the surface water drain from site has been renewed to the brook
- labour & material availability causing delays
- variations costs have been received with the valuations, the break down has been received, with the additional drainage these currently appear to be over the site contingency figure

### Change Control Since Last Meeting

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£771,605.00	£858,800.00	£87,195.00	£860,640.00	

- AML issued Tender Report 04/05/20 - Tender Costs noted
- Risk Items identified have had additional costs allocated in Client Contingency Control budget

### Current RIBA Gateway Position:

Gateway: 4  
 Anticipated completion of current gateway: 02/07/20 (Achieved)

### Key Target Dates

Planning/Amendment Submitted: Submitted  
 Consent Received: 25/01/2017  
 Planning Expiry: 25/01/2020  
 Enacted (Y/N): TBC  
 Start on Site: 11/01/2021  
 Completion: 29/03/2022

## Denny Avenue (Waltham Abbey) - HR144 - Phase 4.2

(1 x 2B4p House & 2 x 3B5p Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£20,511	£20,510	£17,440	£3,070	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£47,908	£47,908	£46,510	£1,398	£0	
3	(Survey Total)	E120	£16,928	£16,928	£16,928	£0	£0	
4	Build Cost	E040	£860,640	£860,640	£606,807	£253,836	£0	
5	(Contingency)	E040	£65,000	£65,000	£0	£64,998	£0	
6	CoW	E180	£4,690	£4,690	£1,392	£3,298	£0	
			<b>£1,015,677</b>	<b>£1,015,677</b>	<b>£689,078</b>	<b>£326,600</b>	<b>£0</b>	



## Denny Avenue (Waltham Abbey) - HR144 - Phase 4.2

(1 x 2B4p House & 2 x 3B5p Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	12	Based on current government advice we are expecting a 3-month delay currently although social distancing may be in effect for up to 6 months	EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed targeted for July, although reduced labour to meet social distancing requirements
<b>Reports &amp; Investigations</b>									
Ground Contamination	4	All sites identified as to having ACMs in made ground.  Denny Avenue - former site of explosives factory - heightened contamination / remediation expected	Contractor / EFDC	2	2	4	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards.  (2) Ground Gas monitoring to be carried out on potentially effected sites subject to lab testing of impacted sites  (3) Remediation Method Statements to be issued where required	
Party Walls - awards to adjoining parties	4	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	1	4	4	EFDC / Keegans	(1) Notices to be served to adjacent properties  (2) PW Surveyor to advise on objections / concerns	Notices served

## Beechfield Walk (Waltham Abbey) - HR142 - Phase 4.2

(5 x 2B4P Houses)

Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	2	4	0
Medium Risk	36	2	0

-

**Actions Complete**

**Forthcoming Actions (Month)**

- Works progressing
- completion date 15/2/22
- off site surface water flooding from field has been assessed, the existing outfall has been utilized by reforming the ditch
- variations costs have been received with the valuations, the break down has been received and these currently appear within the contingency figure. **these have been agreed and to be instructed**

**Change Control Since Last Meeting**

-

**Financial**

**Construction Cost Summary (E040)**

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tdc	£1,087,011.00	£1,297,200.00	£210,189.00	£1,115,482.00	

- AML issued Tender Report 04/05/20 - Tender Costs noted
- Risk Items identified have had additional costs allocated in Client Contingency Control budget

**Current RIBA Gateway Position:**

Gateway:	4	
Anticipated completion of current gateway:	02/07/20	(Achieved)

**Key Target Dates**

Planning/Amendment Submitted:	Submitted
Consent Received:	22/03/2017
Planning Expiry	22/03/2020
Enacted (Y/N)	TBC
Start on Site:	11/01/2021
Completion:	08/02/2022

## Beechfield Walk (Waltham Abbey) - HR142 - Phase 4.2

(5 x 2B4P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£23,664	£23,664	£20,090	£3,574	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£49,558	£49,558	£48,951	£607	£0	
3	(Survey Total)	E120	£20,112	£20,112	£20,112	£0	£0	
4	Build Cost	E040	£1,115,482	£1,115,482	£807,507	£307,975	£0	
5	(Contingency)	E040	£85,000	£85,000	£0	£85,000	£0	
6	CoW	E180	£4,900	£4,900	£1,440	£3,456	£0	
			<b>£1,298,716</b>	<b>£1,298,716</b>	<b>£898,100</b>	<b>£400,612</b>	<b>£0</b>	

## Beechfield Walk (Waltham Abbey) - HR142 - Phase 4.2 (5 x 2B4P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19- Delays	12	Based on current government advice we are expecting a 3-month delay currently although social distancing may be in effect for up to 6 months	EFDC / AML	4	3	12	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed targeted for July, although reduced labour to meet social distancing requirements
<b>Reports &amp; Investigations</b>									
Ground Contamination	3	All sites identified as to having ACMs in made ground.	Contractor / EFDC	1	3	3	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards. (2) Ground Gas monitoring to be carried out on potentially effected sites subject to lab testing of impacted sites (3) Remediation Method Statements to be issued where required	
Party Walls - awards to adjoining parties	4	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	1	4	4	EFDC / Keegans	(1) Notices to be served to adjacent properties (2) PW Surveyor to advise on objections / concerns	Notices Served

## Kirby Close (Loughton ) - HR120 - Phase 4.2

(2 x 3 bed 5p Houses, 2 x 2 bed 4p h Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	0	4	0
Medium Risk	3	3	0

-  
 Actions Complete

### Forthcoming Actions (Month)

- grass island to be temporarily turned into straight across access under licence
- works progressing
- completion 29/3/22
- Sprinklers not required
- nr 20 boundary wall condition under review - it has been agreed with the resident to replace the wall with a fence. Formal signature required
- variations costs have been received with the valuations, the break down has been received and these currently appear within the contingency figure.

Change Control Since Last Meeting

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£911,559.00	£1,107,004.00	£195,445.00	£1,085,101.00	

- AML issued Tender Report 04/05/20 - Tender Costs noted
- Risk Items identified have had additional costs allocated in Client Contingency Control budget

### Current RIBA Gateway Position:

Gateway:	4	
Anticipated completion of current gateway:	02/07/20	(Achieved)

### Key Target Dates

Planning/Amendment Submitted:	Submitted
Consent Received:	22/03/2017
Planning Expiry	22/03/2020
Enacted (Y/N)	TBC
Start on Site:	11/01/2021
Completion:	29/03/2022

## Kirby Close (Loughton) - HR120 - Phase 4.2

(2 x 3 bed 5p Houses, 2 x 2 bed 4p h Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£23,069	£23,069	£19,946	£3,123	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£54,008	£54,008	£53,059	£949	£0	
3	(Survey Total)	E120	£17,577	£17,577	£17,577	£0	£0	
4	Build Cost	E040	£1,085,101	£1,085,101	£661,007	£424,092	£0	
5	(Contingency)	E040	£85,000	£85,000	£0	£85,002	£0	
6	CoW	E180	£4,795	£4,795	£1,350	£3,447	£0	
			<b>£1,269,550</b>	<b>£1,269,550</b>	<b>£752,939</b>	<b>£516,613</b>	<b>£0</b>	

## Kirby Close (Loughton) - HR120 - Phase 4.2

(2 x 3 bed 5p Houses, 2 x 2 bed 4p h Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Programme &amp; Contract Risk</b>									
Programme - COVID-19-Delays	8	Based on current government advice we are expecting a 3-month delay currently although social distancing may be in effect for up to 6 months	EFDC / AML	4	2	8	AML	(1) AML to advise EFDC of obligations under JCT (2) AML to liaise closely with Contractor to establish pre-commencement works (3) Contractor to provide programme considering social distancing guidelines	Risk Reduced - SoS Confirmed targeted for July, although reduced labour to meet social distancing requirements
<b>Reports &amp; Investigations</b>									
Ground Contamination	2	All sites identified as to having ACMs in made ground.	Contractor / EFDC	1	2	2	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards. (2) Ground Gas monitoring to be carried out on potentially effected sites subject to lab testing of impacted sites (3) Remediation Method Statements to be issued	
Trees	0	Trees within vicinity or boundary of site that could impact construction proposals.  Kirby Close 1no tree identified outside of bounday on NW side of site - impacting currnet proposals -	EFDC	0	0	0		(1) Instruction of Aboricultural Surveys to provide comprehensive survey to all sites. Tree Protection Plans & method Statements also commissioned (2) Survey Results to be coordinated with design team to mitigate impact of root protection zones (3) Pick Hill - Liaison with owner of TPO tree's to entrance	Tree agreed to be removed
Party Walls - awards to adjoining parties	3	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	1	3	3	EFDC / Keegans	(1) Notices to be served to adjacent properties (2) PW Surveyor to advise on objections / concerns	

## Pentlow Way (Buckhurst Hill) - HR139 - Phase 4.3

(5 x 1 bed 2p flats, 2 x 2 bed 4p flats)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	1	1	0
Medium Risk	38	1	0

- RoW / Access and Party Wall matters to be determined
- Drainage Build-over Required - Application being progressed
- Levels to East Boundary still to be determined

### Actions Complete

- 
- Allocated parking - not required
- contract prepared to print - programme dates required to produce this, issue date dependant on receiving programme dates and leases being resolved . Start date is slipping. June 2022

### Forthcoming Actions (Month)

- updated tender report approved
- pre start conditions target determination date 2 March
- programme received - sub-station dates to confirm from UKPN - 9 months to agree legals is UKPN target - this will delay start
- site layout for each phase received but to review
- updated UKPN quote received and paid directly by EFDC, contact details received and meeting held. 9 months period for legals indicated by UKPN. Parties are in contact.
- contract in place with TSG
- start June 2022
- neighbours boundary wall to agree
- UKPN revised costs agreed and instructed
- temporary bin position to agree
- site meeting arranged to inspect rear of garages

### Change Control Since Last Meeting

-

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
#REF!	£1,588,896.00	£1,774,636.90	£185,740.90	£1,950,504.00	£0.00

- Order of cost completed and issued Aug 20 construction cost revised
- Tender report issue date 18/9/20

### Current RIBA Gateway Position:

Gateway: 4  
 Anticipated completion of current gateway: 30/10/20

### Key Target Dates

Planning/Amendment Submitted: Submitted  
 Consent Received: 25/01/2017  
 Planning Expiry: 25/01/2020  
 Enacted (Y/N): Yes  
 Start on Site: June 22  
 Completion: June 23



## Pentlow Way (Buckhurst Hill) - HR139 - Phase 4.3

(5 x 1 bed 2p flats, 2 x 2 bed 4p flats)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£34,585	£34,585	£20,383	£14,202	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£91,961	£95,559	£94,198	£1,361	£3,598	ECD to tender figure
3	(Survey Total)	E120	£24,355	£24,355	£23,086	£1,269	£0	
4	Build Cost	E040	£1,950,504	£1,950,504	£0	£1,950,510	£0	
5	(Contingency)	E040	£195,050	£195,050	£0	£195,045	£0	Adjusted to 10% of build cost until Contract cost.
6	CoW	E180	£10,600	£10,600	£0	£10,600	£0	
			<b>£2,307,054</b>	<b>£2,310,652</b>	<b>£137,666</b>	<b>£2,172,987</b>	<b>£3,598</b>	

## Pentlow Way (Buckhurst Hill) - HR139 - Phase 4.3

(5 x 1 bed 2p flats, 2 x 2 bed 4p flats)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	12	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works	EFDC	3	4	12	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained. (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced
Legal issues re: land ownership & stopping-up	0	Subject to completion of Design Review Stage 3 Planning information - ECDA to advise whether amendments are required to adjust redline / boundaries to suit EFDC ownership.  Pentlow Way - Ownership of Dry Area for proposed substation to north of site to be determined	EFDC	0	0	0	EFDC	(1) EFDC to issue ownership and title information (2) AML/ECDA to review impact and advise of any mitigation to current design	Confirmed as EFDC owned Land
<b>Statutory Services &amp; Authorities</b>									
Electric, requirement for new substation(s)	12	New electrical supplies to be sought for new properties - Substation unlikely  Pentlow Way - New Substation required - load capacity to be reviewed and costs associated of extending cables from existing position. - Unrestricted access via undercroft of new building required - minimum height to be confirmed	EFDC	4	3	12	Create (MEP)	(1) Carry out design and obtain capacity check from the service provider. (2) Assess design and space requirements for the new substations	2.5m access height confirmed acceptable by UKPN
Electric / Existing Substation	20	Legal Land Title for the new sub stations and existing stations to be decommissioned and demolished - no existing substations  Pentlow Way - New Substation required - relocation of existing substation to north of site to accommodate new development	EFDC	4	5	20	Create (MEP)	(2) Existing services to be identified and requirement for diversion or abandonment established. (3) EFDC legals to confirm land title status for the existing sub station	
<b>Construction &amp; Procurement</b>									
Programmes - Delays due COVID-19	16	Pre-construction Design Programme Delay to Due Diligence, potential start on site	EFDC / AML	4	4	16	AML	(1) AML preparing programme options, for Stage 4.1 Design schemes and planning redesign schemes. (2) AML to monitor and track government advice on COVID-19	

## Woollard Street (Waltham Abbey) - HR149 - Phase 4.3

(7 x 1B2P & 2B4P Flats)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	3	3	0
Medium Risk	37	1	0

- Contamination Plume identified as localised - risk reduced - Remediation Strategy Confirmed

Actions Complete  
- Tenders received

#### Forthcoming Actions (Month)

- planning application approved 4/2/21
- Updated tender report approved
- update tender drawings to latest planning have been issued on VFP
- Party Wall - Keegans confirmed not required
- temporary closure of access to rear garages will be needed
- discharge pre start conditions by contractor - landscape and materials - this has been submitted but has delayed the start - estimated Feb 2022 - conditions have been validated by planners, decision awaited
- programme received - start date required
- contract signed by TSG
- to run separately from Pentlow
- liaison over access to rear garages to take place - costs to maintain rear access have been agreed and instructed
- pre start meeting held 20/8/21

Change Control Since Last Meeting

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£1,399,539.00	£1,556,186.92	£156,647.92		

- Order of cost completed and issued Aug 20 construction cost revised

- Tender report issue date 18/9/20

#### Current RIBA Gateway Position:

Gateway: 4  
Anticipated completion of current gateway: 30/10/20

#### Key Target Dates

Planning/Amendment Submitted: Submitted  
Consent Received: 25/01/2017  
Planning Expiry: 25/01/2020  
Enacted (Y/N): Yes  
Start on Site: Feb 22  
Completion: Feb 23

## Woollard Street (Waltham Abbey) - HR149 - Phase 4.3

(7 x 1B2P & 2B4P Flats)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£32,388	£32,388	£18,352	£14,036	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£66,564	£68,964	£65,481	£3,483	£2,400	ECD to tender figure
3	(Survey Total)	E120	£50,883	£50,883	£42,604	£8,279	£0	
4	Build Cost	E040	£1,662,008	£1,662,008	£0	£1,662,010	£0	
5	(Contingency)	E040	£166,200	£166,200	£0	£166,208	£0	Adjusted to 10% of build cost until Contract cost.
6	CoW	E180	£10,600	£10,600	£0	£10,600	£0	
			<b>£1,988,644</b>	<b>£1,991,044</b>	<b>£126,437</b>	<b>£1,864,616</b>	<b>£2,400</b>	

## Woollard Street (Waltham Abbey) - HR149 - Phase 4.3

(7 x 1B2P & 2B4P Flats)

### Issues / Risks / Early

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	12	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works  - Vehicle Access to rear of 20-27 Greenfield Street  - Pedestrian Access to rear of Block of flats to Stewardson Street to be maintained	EFDC	3	4	12	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained. (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced
<b>Statutory Services &amp; Authorities</b>									
Drainage Strategy / Sewer Diversions / Abandonments	0	Drainage Strategy to be determined.  Wollard Street - Potential Build-over or major diversion required. Numerous abandonments also required	EFDC	0	0	0	Create (Civil)	(1) Drainage strategy and points of connection to existing sewers to be established, abandonments / diversions to be identified (2) Ownership / adjacent foul connection to be assessed	Drainage Strategy Approved by Thames Water
<b>Reports &amp; Investigations</b>									
Ground Contamination	12	All sites identified as to having ACMs in made ground.	Contractor / EFDC	4	3	12	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards. (2) Ground Gas monitoring to be carried out on potentially effected sites subject to lab testing of impacted sites (3) Remediation Method Statements to be issued	Risk Reduced
Party Walls - awards to adjoining parties	1	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	1	1	1	EFDC / Keegans	(1) Notices to be served to adjacent properties (2) PW Surveyor to advise on objections / concerns	Party wall awards confirmed as not required
<b>Construction &amp; Procurement</b>									
Construction Programmes - Delays due COVID-19	16	Pre-construction Design Programme  Delay to Due Diligence, potential start on site	EFDC / AML	4	4	16	AML	(1) AML preparing programme options, for Stage 4.1 Design schemes and planning redesign schemes. (2) AML to monitor and track government advice on COVID-19	

## Chequers Rd B (Loughton) - HR123 - Phase 4.4

(4 x 1B2P Flats, 4 x 2B4P flats)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	7	0	0
Medium Risk	36	0	0

### Actions Complete

- Sub station - flood levels confirmed by UKPN as not an issue
- Nilan meeting held on their system - system to be used.
- Kitchen layouts - is there space for full height fridge - for purposes of energy usage full height space will be provided subject to adequate storage

### Forthcoming Actions (Month)

- Substation - planning submitted 12/11/20. Determination target 11/1/21 Car chargers are shown - check if can be community.
- Substation build to be included within main tender
- Car chargers for flats 6nr - Create (Chris) to advise 7.5kw per charger - flats allocation to be confirmed
- Start on site moved to Jan 2022 due to delays with planning submissions - will be further delayed by circa 12 months
- Passivhaus - confirm what ER`s are for Passivhaus compliance/requirements (draft to issue -based on 4.3 with addendums for Passivhaus)
- Planning submitted 30/10/2020 Including separate sub station application Target determination 25/12/20
- additional costs of £1197 on flood risk assessment incurred by Create as additional information required than usually expected for planning - to be approved
- TW build over and diversion progress to confirm after Planning
- planners requested dorma detail to be reduced - revised drawings submitted by ECD
- ECD issued remaining Passivhaus tender info
- planners query on sub station parking to replied as Belens response
- planners requested traffic air quality impact assessment which has been issued
- planning committee date 2/2/22
- ERs to review
- tender list to compile

### Change Control Since Last Meeting

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£1,636,993.00	£2,623,385.00	£986,392.00	£1,662,008.00	

- Order of cost updated including garden landscaping, sub station and parking

### Current RIBA Gateway Position:

Gateway: 3  
Anticipated completion of current gateway: 31/10/2020

### Key Target Dates

Planning/Amendment Submitted: 30/10/2020  
Consent Received: 09/02/2016  
Planning Expiry: 09/02/2019  
Enacted (Y/N): Yes  
Start on Site: Jan 23  
Completion: Jan 24

## Chequers Rd B (Loughton) - HR123 - Phase 4.4

(4 x 1B2P Flats, 4 x 2B4P flats)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£37,968	£37,969	£12,035	£25,934	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£93,052	£93,052	£87,983	£5,069	£0	
3	(Survey Total)	E120	£59,174	£59,174	£37,146	£22,028	£0	
4	Build Cost	E040	£2,623,385	£2,623,385	£0	£2,623,385	£0	
5	(Contingency)	E040	£262,339	£262,339	£0	£262,344	£0	Updated to 10% of build cost
6	CoW	E180	£6,800	£6,800	£0	£6,800	£0	
			<b>£3,082,718</b>	<b>£3,082,719</b>	<b>£137,164</b>	<b>£2,945,560</b>	<b>£0</b>	

## Chequers Rd B (Loughton) - HR123 - Phase 4.4

(4 x 1B2P Flats, 4 x 2B4P flats)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	4	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works	EFDC	1	4	4	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained. (2) EFDC to confirm timescales / impact of any delayed liaison with	04/12/19 - EFDC advised legal team are progressing matters - risk reduced
<b>Planning Approvals</b>									
New Planning Application	20	New Proposals to be reviewed - subject to re-briefing meeting. Likely however new application will be required.	EFDC	4	5	20	ECDA/ Create	(1) EFDC to provide briefing details to inform capacity review. (2) ECDA to liaise with EFDC Planners and ensure consistent pre-app discussions are held. (3) ECDA to continue RIBA 1-3 design development	Targeted for Mid-August Now mid October
Consultation Issues - Planning Refusal	15	If new application is submitted, risk of refusal or objection a risk. Furthermore - delay to approval of Local plan leading to delay in planning application approval.	EFDC	3	5	15	EFDC	(1) EFDC to liaise with EFDC Planners on redesign sites - ongoing pre-app discussions to mitigate risk of objection or refusal	
<b>Statutory Services &amp; Authorities</b>									
Drainage Strategy / Sewer Diversions / Abandonments	16	Drainage Strategy to be determined. Potential Build-over or major diversion required.	EFDC	4	4	16	Create (Civil)	(1) Drainage strategy and points of connection to existing sewers to be established, abandonments / diversions to be identified (2) Ownership / adjacent foul connection to be assessed	
<b>Reports &amp; Investigations</b>									
Flood Risk	12	Post Planning - Flood Risk consultant has identified this site to have heightened risk of surface water flooding. EFDC Drainage Engineer's have advised "to raise finish floor levels to at least	EFDC	3	4	12	FRA Consultant + Create (Civil)	(1) Flood Risk Modelling to be carried out (2) Buildings FFL to be raised 300mm above existing ground level (3) Details to issued to	FFL raised to address Flood Risk concerns - redesign ongoing
Electric, requirement for new substation(s)	12	New electrical supplies to be sought for new properties - Substation unlikely New Substation required - load capacity to be reviewed and costs associated of extending cables from existing position. - Unrestricted access via undercroft of new building required - minimum	EFDC	3	4	12	Create (MEP)	(1) Carry out design and obtain capacity check from the service provider. (2) Assess design and space requirements for the new substations	
Electric / Existing Substation	20	Legal Land Title for the new sub stations and existing stations to be decommissioned and demolished - no existing substations Relocation of existing substation to north of site to accommodate new development	EFDC	4	5	20	Create (MEP)	(1) Obtain utility service records. (2) Existing services to be identified and requirement for diversion or abandonment established. (3) EFDC legals to confirm land title status for the existing sub station	
<b>Pre-Construction &amp; Procurement</b>									
Pre-Construction Programmes - Delays due COVID-19	16	Pre-construction Design Programme Delay to Due Diligence, potential start on site	EFDC / AML	4	4	16	AML	(1) AML preparing programme options, for Stage 4.1 Design schemes and planning redesign schemes. (2) AML to monitor and track government advice re COVID-19	



# Ladyfields (Loughton) - HR125 - Phase 4.4

(2 x 2B4P Houses, 2 x 3B4P Houses & 12 x 1B2P Flats)

**Issues / Risks / Early Warning**

Risk Register			
	Risks	Mitigated	Overdue
High Risk	5	0	0
Medium Risk	37	1	0

**Actions Complete**

**Forthcoming Actions (Month)**

- planning submitted 10/9/20 - target determination date 14/12/2020 - not achieved
- request to change elevation drawings sent to planners (potential NMA if not approved)
- BT Telegraph pole removal progressed with Openreach - quote received - order to place once next steps agreed - confirm timescales with BT 5-7 weeks
- Target date for issuing tenders will be after planning approved
- Start on site estimated Jan 2022 - this will be delayed further due to planning
- three framework contractors have the appetite for a Passivhaus scheme
- Car charging direct to allocated parking to house
- tenders not to be issued until planning approved
- Contamination gas protection -CS3 (score 4.5) - ventilated floor void required - proposals provided
- drainage, trees - objections being closed
- planners requested traffic air quality impact assessment which has been issued
- planning committee date 2/2/22
- ERs to review
- tender list to compile

**Change Control Since Last Meeting**

-

**Financial**

**Construction Cost Summary (E040)**

Cabinet Approved Construction Cost	Initial Build Cost Estimate (Jan 18)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date (+/-)
tbc	£1,275,879.00	£3,681,662.00	£2,405,783.00	£0.00	£0.00

- Order of cost completed and issued July 20 construction cost revised

**Current RIBA Gateway Position:**

Gateway: 3  
 Anticipated completion of current gateway: 11/12/2020

**Key Target Dates**

Planning/Amendment Submitted: 10/09/2020  
 Consent Received:  
 Planning Expiry  
 Enacted (Y/N)  
 Start on Site: Jan23  
 Completion: Jan 24

## Ladyfields (Loughton) - HR125 - Phase 4.4

(2 x 2B4P Houses, 2 x 3B4P Houses & 12 x 1B2P Flats)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£75,353	£75,353	£22,869	£52,484	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£168,953	£168,953	£156,984	£11,969	£0	
3	(Survey Total)	E120	£58,090	£58,090	£41,350	£16,740	£0	
4	Build Cost	E040	£3,681,662	£3,681,662	£0	£3,681,662	£0	
5	(Contingency)	E040	£368,166	£368,166	£0	£368,175	£0	Adjusted to 10% of Build cost budget
6	CoW	E180	£14,800	£14,800	£0	£14,800	£0	
			<b>£4,367,024</b>	<b>£4,367,024</b>	<b>£221,203</b>	<b>£4,145,830</b>	<b>£0</b>	

## Ladyfields (Loughton) - HR125 - Phase 4.4

(2 x 2B4P Houses, 2 x 3B4P Houses & 12 x 1B2P Flats)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	12	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works  Access for TFL / NR to track to SE rear corner of site	EFDC	3	4	12	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained. (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced
<b>Planning Approvals</b>									
New Planning Application	20	New Proposals to be reviewed - subject to re-briefing meeting. Likely however new application will be required.	EFDC	4	5	20	ECDA/ Create	(1) EFDC to provide briefing details to inform capacity review. (2) ECDA to liaise with EFDC Planners and ensure consistent pre-app discussions are held. (3) ECDA to continue RIBA 1-3 design	Submission made
Consultation Issues - Planning Refusal	15	If new application is submitted, risk of refusal or objection a risk.  Furthermore - delay to approval of Local plan leading to delay in planning application	EFDC	3	5	15	EFDC	(1) EFDC to liaise with EFDC Planners on redesign sites - ongoing pre-app discussions to mitigate risk of objection or refusal	
<b>Statutory Services &amp; Authorities</b>									
Electric / Existing Substation	0	Legal Land Title for the new sub stations and existing stations to be decommissioned and demolished -  Ladyfields - Existing Substation located in close proximity of NW boundary of site. HV/LV cable routes currently unknown - Access and easement requirement to be	EFDC	0	0	0	Create (MEP)	(1) Obtain utility service records. (2) Existing services to be identified and requirement for diversion or abandonment established. (3) EFDC legals to confirm land title status for the existing sub station	Confirmed no impact to our boundary or scheme
<b>Reports &amp; Investigations</b>									
Ground Contamination	15	All sites identified as to having ACMs in made ground.	Contractor / EFDC	5	3	15	Contractor	(1) Soil Analysis Plans (SAPs) agreed with EFDC contamination team to ensure all necessary analysis is to EFDC standards. (2) Ground Gas monitoring to be carried out on potentially effected sites subject to lab testing of impacted sites (3) Remediation Method Statements to be issued where required	
Trees	12	Trees within vicinity or boundary of site that could impact construction proposals.  Ladyfields - substantial impact to site by number of mature tree's - heavily restrains capacity and design proposals	EFDC	4	3	12		(1) Instruction of Arboricultural Surveys to provide comprehensive survey to all sites. Tree Protection Plans & method Statements also commissioned (2) Survey Results to be coordinated with design team to mitigate impact of root protection zones (3) Ladyfields - Liaison with EFDC in regards to removal of 2nd large mature tree to open up development site	Current proposals accommodate Root Protection zones - risk reduced
Party Walls - awards to adjoining parties	15	Party Wall Adjacent Excavation and Line of Junction Awards required	EFDC	3	5	15	EFDC / Keegans	(1) Notices to be served to adjacent properties (2) PW Surveyor to advise on objections / concerns	
<b>Pre-Construction &amp; Procurement</b>									
Pre-Construction Programmes - Delays due COVID-19	16	Pre-construction Design Programme  Delay to Due Diligence, potential start on site	EFDC / AML	4	4	16	AML	(1) AML preparing programme options, for Stage 4.1 Design schemes and planning redesign schemes. (2) AML to monitor and track government advice on COVID-19	

## Lower Alderton Hall Lane (Loughton) - HR121 - Phase 4.4

(2 x 2B4P Houses)

### Issues / Risks / Early Warning

Risk Register			
	Risks	Mitigated	Overdue
High Risk	3	0	0
Medium Risk	35	1	0

- Lower Alderton planning 25/09/19 - risk is refusal.
- Risk of resident objection and disruption to works
- Pedestrian RoW to be maintained during works to access beneath footbridge
- Contamination risk present on site

### Actions Complete

- Tender Return 02/03/20 - scheme to be omitted due to SAC delay

### Forthcoming Actions (Month)

- Lower Alderton - likely subject to S106 Agreement relating to Natural England's Air Quality Issues
- procurement route to be considered once planning approved

### Change Control Since Last Meeting

### Financial

#### Construction Cost Summary (E040)

Cabinet Approved Construction	Initial Build Cost Estimate (Jan)	Latest Pre-Tender Estimate	Variance from initial Estimate (+/-)	Build Cost (Tender Figure Fixed)	Build Variations To Date
tbc	£507,768.00	£761,467.00	£253,699.00	£0.00	£0.00

### Current RIBA Gateway Position:

- Gateway: 4
- Anticipated completion of current gateway: TBC
- Tender Return 02/03/20 - scheme to be omitted due to SAQ delay

### Key Target Dates

- Planning/Amendment Submitted: Submitted - New Application (TBC)
- Consent Received: 09/02/2016
- Planning Expiry: 09/02/2019
- Enacted (Y/N): Yes
- Start on Site: Jan 2022
- Completion: Dec 2023

## Lower Alderton Hall Lane (Loughton) - HR121 - Phase 4.4

(2 x 2B4P Houses)

### Development Cost Movement Report

	Description	Cost Code	Previous Contract Total	Contract Total	Total Invoiced	Total Remaining	Variance	Reason for Movement
1	Airey Miller Fees	E130	£18,361	£18,361	£13,614	£4,747	£0	
2	ECDA, Create, Keegans & OHLA Fees	E160	£42,738	£42,738	£41,879	£859	£0	
3	(Survey Total)	E120	£23,481	£23,481	£21,736	£1,745	£0	
4	Build Cost	E040	£554,700	£554,700	£0	£554,700	£0	
5	(Contingency)	E040	£55,470	£55,470	£0	£55,476	£0	
6	CoW	E180	£10,800	£10,800	£0	£10,800	£0	
			<b>£705,550</b>	<b>£705,550</b>	<b>£77,229</b>	<b>£628,327</b>	<b>£0</b>	

## Lower Alderton Hall Lane (Loughton) - HR121 - Phase 4.4

(2 x 2B4P Houses)

### Issues / Risks / Early Warning

Hazard/Risk	PxI	Comments	Risk Owner	Probability 1-5	Impact 1-5	P x I Score	Action By	Control Measures	Outcomes
<b>Land, Ownership and Acquisition</b>									
Rights of Way Disruption to Adjoining Residents & the general public	12	Public Access or Rights of Way preventing proposed construction. Disruption to Neighbours potentially delaying on-site works  - Surrounding Houses (Nr 1-11) - RoW / Access Rights to existing Parking - to be determined. Site to be appropriated  - RoW to access under bridge leading to Bushfields site to be maintained	EFDC	3	4	12	EFDC	(1) EFDC to ascertain progress with legals on extinguishment or access RoW required to be maintained.  (2) EFDC to confirm timescales / impact of any delayed liaison with residents	04/12/19 - EFDC advised legal team are progressing matters - risk reduced  29/01/20 - Meeting held 20/01/20. Sites being assessed by EFDC legal consultant for any RoW or access rights. EFDC to advise.
<b>Planning Approvals</b>									
Planning Requirements - S106 Agreement	16	Natural England Requirements for Air Quality Mitigation - likely to be packaged into S106 Agreement - negotiation required	EFDC	4	4	16	EFDC	EFDC to liaise with Residents and advise of leasehold garden areas to be avoided	29/01/20 - No response to date
Consultation Issues - Planning Refusal	15	Lower Alderton - Local Residents objected original consent - re-submitted in May - Committee Meeting 25/09/19 - No	EFDC	3	5	15	EFDC	(1) EFDC to liaise with EFDC Planners to confirm discharge of necessary conditions	
<b>Reports &amp; Investigations</b>									
Ground Contamination	16	Potential for Ground Gas Identified in Phase Geotechnical Report	Contractor / EFDC	4	4	16	Contractor	(1) Contractor to confirm allowance within tender for removal of interceptors and contaminated soil	
Pre-Construction Programmes - Delays due COVID-19	16	Pre-construction Design Programme  Delay to Due Diligence, potential start on site	EFDC / AML	4	4	16	AML	(1) AML preparing programme options, for Stage 4.1 Design schemes and planning redesign schemes. (2) AML to monitor and	
