Epping Forest District Council Corporate Risk Register

Date: 18 September 2014

Contents

Section		Page No.
1.	Introduction	3
2.	The Process	4
Appendix 1	Risk Profile	6
Appendix 2	Corporate Risk Register /Action Plans	7 - 18

1. Introduction

A strategic risk management 'refresh' exercise was conducted on 15th May 2013 with assistance from Zurich Risk Engineering. This exercise was an opportunity for the Management Board to refresh (or update) through identification, analysis and prioritisation those risks that may affect the ability of the Council to achieve its strategic objectives and Corporate Plan. In doing so, the organisation is recognising the need to sustain risk management at the highest level.

The refresh exercise involved a workshop with Management Board to identify new business risk areas and to update and re-profile important risks from the existing corporate risk register.


In total 8 strategic risks were profiled at the workshop and during the workshop, each risk was discussed to ensure common agreement and understanding of its description and then prioritised on a matrix. The risk matrix measured each risk for its likelihood and its impact in terms of its potential for affecting the ability of the organisation to achieve its objectives.

For the risks that were assessed with higher likelihood and impact, the group validated the risk scenarios and determined actions to manage them, including assessing the adequacy of existing actions and identifying the need for further actions in order to move the risk down the matrix.

Management Board agreed a timescale for re-visiting these risks in order to assess if they are still relevant and to identify new scenarios. Risks in the red zone will be monitored on a monthly basis and those in the amber zone on a quarterly basis.


The following report outlines the process utilised by Zurich Risk Engineering and the results achieved.

2. The Process

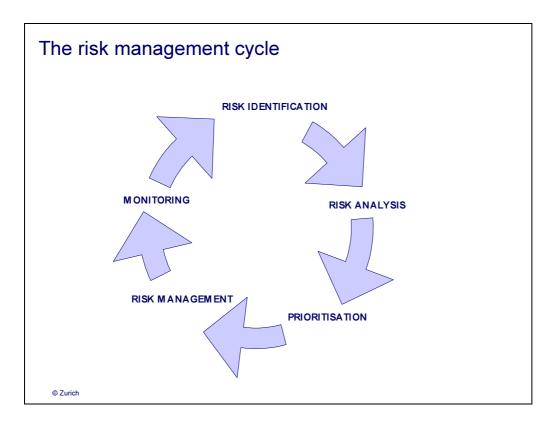

Risk identification

The first of five stages of the risk management cycle requires risk identification. This formed the initial part of the workshop. In doing so the following 13 categories of risk were considered.

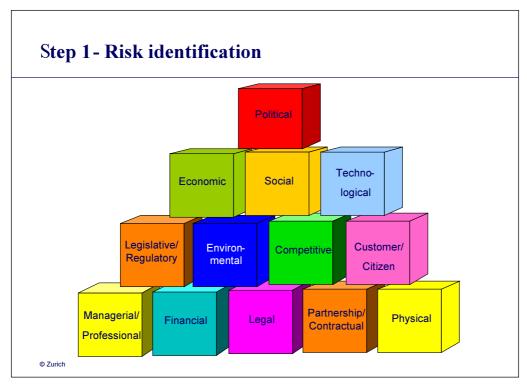

Risk analysis

During the workshop, the identified risks were discussed and framed into a risk scenario format, containing risk cause and consequence elements, with a 'trigger' also identified, This format ensured that the full nature of the risk was considered and also helped with the prioritisation of the risks.

Risk prioritisation

The discussion resulted in 8 risk scenarios being agreed (Appendix 2) and these were then assessed for impact and likelihood and plotted onto a matrix (Appendix 1). The likelihood of the risks was measured as being 'very high', 'high', 'medium', or 'low/very low'. The impact, compared against the key objectives and Corporate Plan was measured as being 'major', 'moderate', 'minor' or 'insignificant'.

Once all risks had been plotted the matrix was overlaid with red, amber and green filers, with those risks in the red area requiring further particular scrutiny in the short-term, followed by those in the amber area.

Risk management and monitoring

The next stage is to monitor the revised management action plans. These plans frame the risk management actions that are required. They map out the target for each risk i.e. to reduce the likelihood, impact or both. They also include targets and critical success factors to allow the risk management action to be monitored.

A risk owner has been identified for each risk. It is vital that each risk should be owned by a member of Management Board to ensure that there is high level support, understanding and monitoring of the work that is required as part of the plans. Risks should also be reviewed as part of the business planning process, in order to assess if they are still relevant and to identify new issues.


The monitoring of these action plans takes place at Corporate Governance Group, Management Board and the Risk Management Group. The action plans are also reported to Members quarterly.

As part of the regular review and reporting an additional risk on Safeguarding was added to the register in January 2014.

Appendix 1 – Risk Profile

Risk profile

During the workshop, 8 risks were identified and framed into scenarios. The results are shown on the following risk profile.

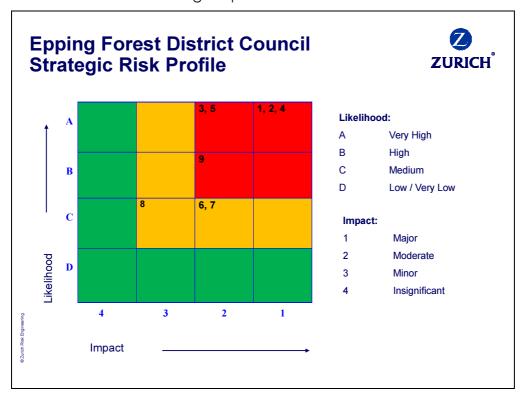

Appendix 2 details all of the above risks.

It is important that an action plan element is written for each of the risks, with particular focus on those with the highest priority, as it is this which will allow them to be monitored and successfully managed down.

An opportunity was also taken as part of this refresh to 'spring clean' the risk numbers, and they were numbered in priority order as follows:

New risk number	Short name
1	Local plan
2	Strategic sites
3	Welfare reform
4	Finance – income
5	Economic development
6	Data/information
7	Business continuity
8	Partnerships
9	Safeguarding

Appendix 2 – Corporate Risk Register and Action Plans

Risk No 1 Local Plan A1			
Vulnerability	Trigger	Consequence	Risk Owner
On-going changes to Planning system increase importance of having up to date Local Plan.	Failure to make timely decisions and adhere to Local Development Scheme Project Plan.	Reduced ability to manage development in line with local priorities. Failure to provide strategic direction for future development, and housing etc for future needs.	Derek Macnab
Changes in government planning policy require new Local Plan to take approaches significantly different from predecessors eg Duty to Co-operate, release Green Belt.	Failure of Council to approve a draft plan in line with National Planning Policy Framework.	Plan not "sound", leading for further delay, wasted resources, and vulnerability to planning appeal decisions.	
Difficulties in implementing "Duty to Co-operate" may make it difficult or impossible to achieve "sound" Local Plan in timely fashion	Inability to agree, particularly on amount and distribution of objectively assessed development needs.	As above	
Failure to make timely progress increases likelihood of "planning by appeal"	Failure to adhere to Local Development Scheme leads to developers making significant planning applications in advance of new Plan.	Significant diversion of professional resources to appeals. Risk of costs awards against Council. Potential lost opportunity for infrastructure and other provision due to outdated/National Planning Policy Framework non-compliant policies Development which is inappropriate in location/scale/type	
Lack of adopted Plan reduces ability to obtain developer contributions.	Developers exploit inadequacies in S106/CIL arrangements.	Additional demands put on public funding of infrastructure.	
Loss/sickness of key staff and recruitment difficulties or inappropriate resource provision hold back progress.	Loss/long term absence of key staff.	Delay in progress Potential need for rework due to loss of "corporate memory".	

Risk No 1 Local Plan –	Action Plan					
Existing Controls/actions to address risk	Effectiveness of controls/actions	Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date
Project management approach in place including regular updates, resource planning.	Project plan needs to incorporate more time for political engagement at key decision points.	Agree mechanisms and timing with lead members, incorporate in revised project plan	Derek Macnab	Future adherence to project plan.	Project plan ongoing. MB review 6 weekly	Finalise key evidence esp. re development need to summer 2014. Cabinet to agree draft plan for consultation September 2014, Consultation November 2014- January 2015.
Local Development Scheme revised July 2014.	Local Development Scheme adopted by Cabinet 21 July 2014.	Review Local Development Scheme on basis of new project plan, (see above)	Derek Macnab	Local Development Scheme remains robust	As necessary	Review likely within 12 months
Workshops for EFDC and Town/Parish councillors on key issues to enhance awareness and understanding of new government requirements.	Workshops popular and helpful but not a mechanism for strategic decision making.	Supplement workshops with other forms of briefing to EFDC members as agreed with leading members.	Derek Macnab	Timely decision making in line with project plan.	As necessary	
Engagement with other key stakeholders eg ad hoc meetings with Town/Parish councils, Resident Associations, use of Forester and website.	Limited, as tends to be reactive, resource intensive, and consistent messages difficult to develop in light of uncertainties over project plan	Develop strategic communications plan and implement See above re project plan	Derek Macnab	Stakeholders feel well informed about process and decisions. Informed responses to public consultation. Less need for reactive communications.	As necessary	Establish communications approach by mid September 2014

Existing Controls/actions to address risk	Effectiveness of controls/actions	Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date
Systematic approach to Duty to Co-operate, engaging public bodies and developing Memorandum of Understanding with key councils in the Strategic Market Housing Area.	Difficulties and delay in engaging councils in serious discussion re Memorandum of Understanding, however progress now being made. meetings held with most other key bodies with positive outcomes, issues identified. Constant review of Planning Institute local plan decisions re Duty to Co-operate.	Important that key decisions do not precede Duty to Co-operate ie "fait accompli"- needs to be accommodated in project plan and Local Development Scheme. Progress Memorandum of Understanding, engaging members and using Planning Advisory Service support as necessary. Engage further key bodies eg Lee Valley Regional Park. Discuss informally with Planning Institute as necessary.	Derek Macnab	Submitted plan passes legal test of Duty to Cooperate.	MB review six weekly	Officer Meetings – monthly now underway Member briefing by PAS 25 March. Further Member meetings to finalise Governance arrangements and "Duty to C0-operate planned for September 2014.
Consultants in place to support project management, resource planning, Sustainability Assessment, transport modelling, masterplanning. Experienced maternity cover for key posts in place. Temporary posts resourced. Budget available.	Staff cannot be prevented from leaving. Exit interviews should reveal any specific patterns. Market is picking up, making recruitment more difficult. Review of Staffing undertaken.	Review of Strategy agreed by Management Board. Implementation.	Derek Macnab	No delays to timetable due to staffing gaps or lack of critical skills	As above	New Staffing Structure Implemented by October 2014.

Risk No 2 Strategic Site	es A1						
Vulnerability		Trigger		Consequence			Risk Owner
The Council has a number of Strategic sites which it needs to make the right decisions about and then deliver on those decisions.		Not maximising the opportunity of the strategic sites either through decisions or delivery		 Financial viability of Council harmed Lack of economic development and job creation External criticism 			Colleen O'Boyle
Existing Controls/actions to address risk			Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date
Work on strategic sites is co- ordinated through a dedicated Cabinet Committee.	Work is progressing developing a number of the work has now commenced on site redevelop the Winst Churchill site; 2. Draft Heads of T St Johns Road agree Cabinet in July; 3. The re-letting of contract has freed under the work of the	to to ton ferms for eed by the waste up ier than d; ster	Reports to Cabinet Committee and Cabinet to obtain decisions on development options.	Colleen O'Boyle	Development of strategic sites completed in accordance with Cabinet decisions.	Monthly	None

Risk No 3 Welfare Reform	n A2							
Vulnerability		Trigger		Consequence			Risk Owner	
the welfare system which is likely to have serious detrim			eform changes have a al effect on the Council and ry	 Tenants no longer able to afford current/new tenancies. Increase in evictions and homelessness Increased costs of temporary accommodation Unable to secure similar level of income due to payment defaults Increase in rent arrears Public dissatisfaction Criticism of the Council for not mitigating the effects for residents. 			Alan Hall	
Existing Controls /actions to address risk	Effectivenes controls/acti	• • •	Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date	
Joint Benefits and Housing working group established. Mitigation action plan developed.	Two thirds of the actions have been implemented and the remaining actions are in		Working Group to continue and amend mitigation action plan as necessary.	Alan Hall	A smooth implementation of welfare reforms. Minimise number and cost of redundancies.	Monthly	Start date for Universal Credit still unclear	

Risk No 4 Finance Income	e A1						
Vulnerability		Trigger		Consequence			Risk Owner
The Council has a reliance on major income generating contracts and fee earning services. Some of which have been adversely affected by the recession and some of which may be affected by legislative change. With changes to central funding based on local		Unable to secure required level of income due to recession, reduced economic confidence or adverse change in funding		 Staffing and s Increase Cou Increase in ch Greater use of achieved 	narges f reserves if required net sa	vings not	Bob Palmer
retention of NDR the Council is more vulnerable to downturns in the local economy and to the large number of outstanding appeals against NDR assessments that pre-date local retention but which the Council will have to fund.				Higher level of	f saving in subsequent year	'S.	
Welfare reform may require sub- the calculation and administratio likely reduction in funding receiv	n of benefits with a						
The medium term financial strate substantial net CSB reductions of							
Existing Controls /actions to address risk	Effectivenes controls/act		Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date
Monitoring of key income streams and NDR tax base. Savings opportunities pursued through service reviews and corporate restructure.	Effective to date as budgets have been achieved that meet the financial targets set by Members.		Update Medium Term Financial Strategy as announcements are made on changes to central funding and welfare. Continue to pursue opportunities to reduce net spending.	Bob Palmer	Savings targets achieved with net expenditure reductions over the medium term as part of a structured plan.	Monthly	17 February 2015 Council adopt budget for 2015/16

Vulnerability		Trigger		Consequence			Risk Owner
Economic development and employment is very important, particularly in the current economic climate. The Council needs to be able to provide opportunities for economic development and employment (especially youth employment) in the District.			erforms relatively poorly I to other authorities.	 Unable to secure sufficient opportunities Local area and people lose out Insufficient inward investment Impact on economic vitality of area Loss of revenue 			Colleen O'Boyle
Existing Controls/actions to address risk	Effectivenes controls/act		Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date
Work has commenced on an updated Economic Development Strategy. Report to September Cabinet seeking four new posts.	Resources in this a not yet been increa with the greater sig it now has.	sed in line	Completion of Strategy and allocation of appropriate resources. Recruitment of experienced staff.	Colleen O'Boyle	Growth in NDR tax base and employment opportunities. Council to be viewed as punching above its weight.	Monthly	30 September 2014 – target date for completion of strategy.

Vulnerability		Trigger		Consequence		Risk Owner	
The Authority handles a large amount of personal and business data. Either through hacking or carelessness, security of the data could be compromised.		Data held by the Council ends up in inappropriate hands.		 Breach of corporate governance Increased costs and legal implications Reputation damaged 			Bob Palmer
Existing Controls/actions to address risk	Effectivenes controls/acti		Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date
Security Officer is continually monitoring situation and potential risks. Most systems have in built controls to prevent unauthorised access. Controls in systems have been strengthened in response to specific occurrences Rollout of a Data Protection elearning module commenced Jan 2014, for completion by officers every two years. Data Protection formed part of Member induction from May 2014, with requirement to confirm acceptance of the Council's DP policy.	Generally effective with only minor laps 2013/14.		Maintain GCSx compliance and system controls. Consolidation of Data Protection and Freedom of Information work in one area.	Bob Palmer	No data loss or system downtime due to unauthorised access of EFDC systems or data. Continued security of personal data held by the Council in accordance with the Data Protections Act 1998.	Quarterly	None

Vulnerability		Trigger		Consequence			Risk Owner
The Council is required to develop and implement robust Business Continuity Plans in line with the requirements of the Civil Contingencies Act. Following the consolidation into four directorates plans need to be updated and changes in responsibilities confirmed.		Unable to respond effectively to a business continuity incident (e.g IT virus/flu pandemic)		 Services Possible I Staff abse Hardship Council or 	Derek Macnab		
Existing Controls/actions to address risk	Effectiveness of controls/actions		•	Responsibility for action	Critical success factors and measures	Review frequency	Key date
Most services already have business continuity plans in place and a separate flu pandemic plan has been developed.	The effectiveness of is assessed periodic through test and ex	cally	Both corporate and service business continuity plans are being updated. Implementation of Cabinet approved measures to enhance the resilience of ICT	Derek Macnab	Having plans in place which are proved fit for purpose either by events or external scrutiny.	Quarterly	None

Risk No 8 Partnerships	C3						
Vulnerability		Trigger		Consequence		Risk Owner	
The Council is involved in a plethora of multi agency partnerships e.g. LSP - LEP, and these have a variety of governance arrangements. Localism act may cause transfer of Council services to providers with governance issues.		provided	ership fails or services via arrangements lacking governance.	Relationships with other bodies deteriorate Glaw back of grants			Glen Chipp
Existing Controls/actions to address risk	Effectiveness of controls/actions		Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date
Active participation in key partnerships by appropriate officers/Members. Structured reporting back to designated Scrutiny Panels. Members can request representatives on outside bodies to report to Full Council.	No significant issue However, some con exists about the wo the North Essex Pa Partnership.	ncern orking of	Continue existing monitoring procedures for current partnerships and construct appropriate arrangements for any new partnerships.	Glen Chipp	No significant impacts on service delivery or Council reputation from any partnership failures.	Quarterly	None

Vulnerability	Trigger	Consequence	Risk Owner	
The Council needs to demonstrate its ability to meet its duties under Sections 11 and 47 of the Children Act 2004. Although not yet a statutory requirement, the Council also needs to comply with best practise in regard to safeguarding vulnerable adults from narm. This is a Council –wide requirement which includes training and awareness of staff at all levels across the organisation and Elected Members. Effective systems and processes for safeguarding children, young people and vulnerable adults need to be in place. The Council needs to ensure that key contractors have systems in place, and that there are staff trained, to identify and report safeguarding concerns appropriately.	The Council fails to meet its duties in regard to safeguarding and information sharing Elected Member reluctance to undertake training results in the Council failing to meet a 'whole Council' approach Staff reluctance to be involved in referring safeguarding concerns due to lack of confidence and awareness.	 A child, young person or vulnerable adult suffers significant harm A child, young person or vulnerable adult suffers from exploitation Avoidable death of a child, young person or vulnerable adult living in the District Reputational risk for Council Censure and special measures applied 	Alan Hall	

Risk No 9 Safeguarding - Action Plan								
Existing Controls/ actions to address risk	Effectiveness of controls/actions	Required further management action	Responsibility for action	Critical success factors and measures	Review frequency	Key date		
The Council has a current and comprehensive Safeguarding Policy which is updated annually or in line with any changes within legislation. The policy details what is required of all staff and members, and contains clear instructions for the recording and processing of safeguarding concerns, incidents and allegations.	The Council has reduced the risk of safeguarding issues going unnoticed by staff and members by providing clear procedures and requirements for training and awareness.	Leadership Team and Managers to ensure that all staff are aware of the Councils safeguarding policy and procedures The Council needs to ensure timely response to changes in legislation or local procedures.	Alan Hall	The Council meets all of its duties under Section 11 and 47. The Council fully meets all aspects of the ESCB/ESAB Safeguarding self - assessment.	Monthly	Monthly		
Corporate Safeguarding Group is forum for sharing best practice and information across Directorates and identifying any weaknesses in the Council's work.	This group is only partially effective, due to limited commitment by some Directorates	Directorates need to commit time for representatives to attend the Corporate Working Group.						
Contractors safeguarding processes are included in the procurement process. All staff are required to undertake appropriate safeguarding training. The Council has a Safe Recruitment Policy.	Room for improvement. This will be effective subsequent to a training Plan being developed.	Need to ensure they have appropriate systems to address safeguarding issues. Staff require training in Safe Recruitment.						
The Council has a dedicated senior safeguarding post for two years to enable the Council to meet all of the required standards.	Safe Recruitment assists the Council in reducing the risk of employing an unsuitable member of staff.							
